

SECTION D: EROSION AND SEDIMENT CONTROL PLANS

SD DOT	PROJECT	SECTION	SHEET
	NH-B 0212(194)266	D1	D19
Plotting Date: 06/22/2026			

INDEX OF SHEETS

D1	General Layout with Index
D2-D5	Estimate with General Notes and Tables
D6-D9	Stormwater Pollution Prevention Plan Checklist
D10	Erosion and Sediment Control Legend
D11-D12	Erosion and Sediment Control Plan Sheets
D13	Dewatering and Sediment Collection System Details
D14	SDDOT Construction Entrance Details
D15-D19	Standard Plates




BEGIN GRADING NH-B 0212(194)266
South Fork Snake Creek
Station 1114+59.11 =

**END GRADING
BEGIN AC RESURFACING**
Station 1123+26.36

BEGIN & END ADA WORK

**END NH-B 0212(194)266
END AC RESURFACING**
Station 1188+46.00

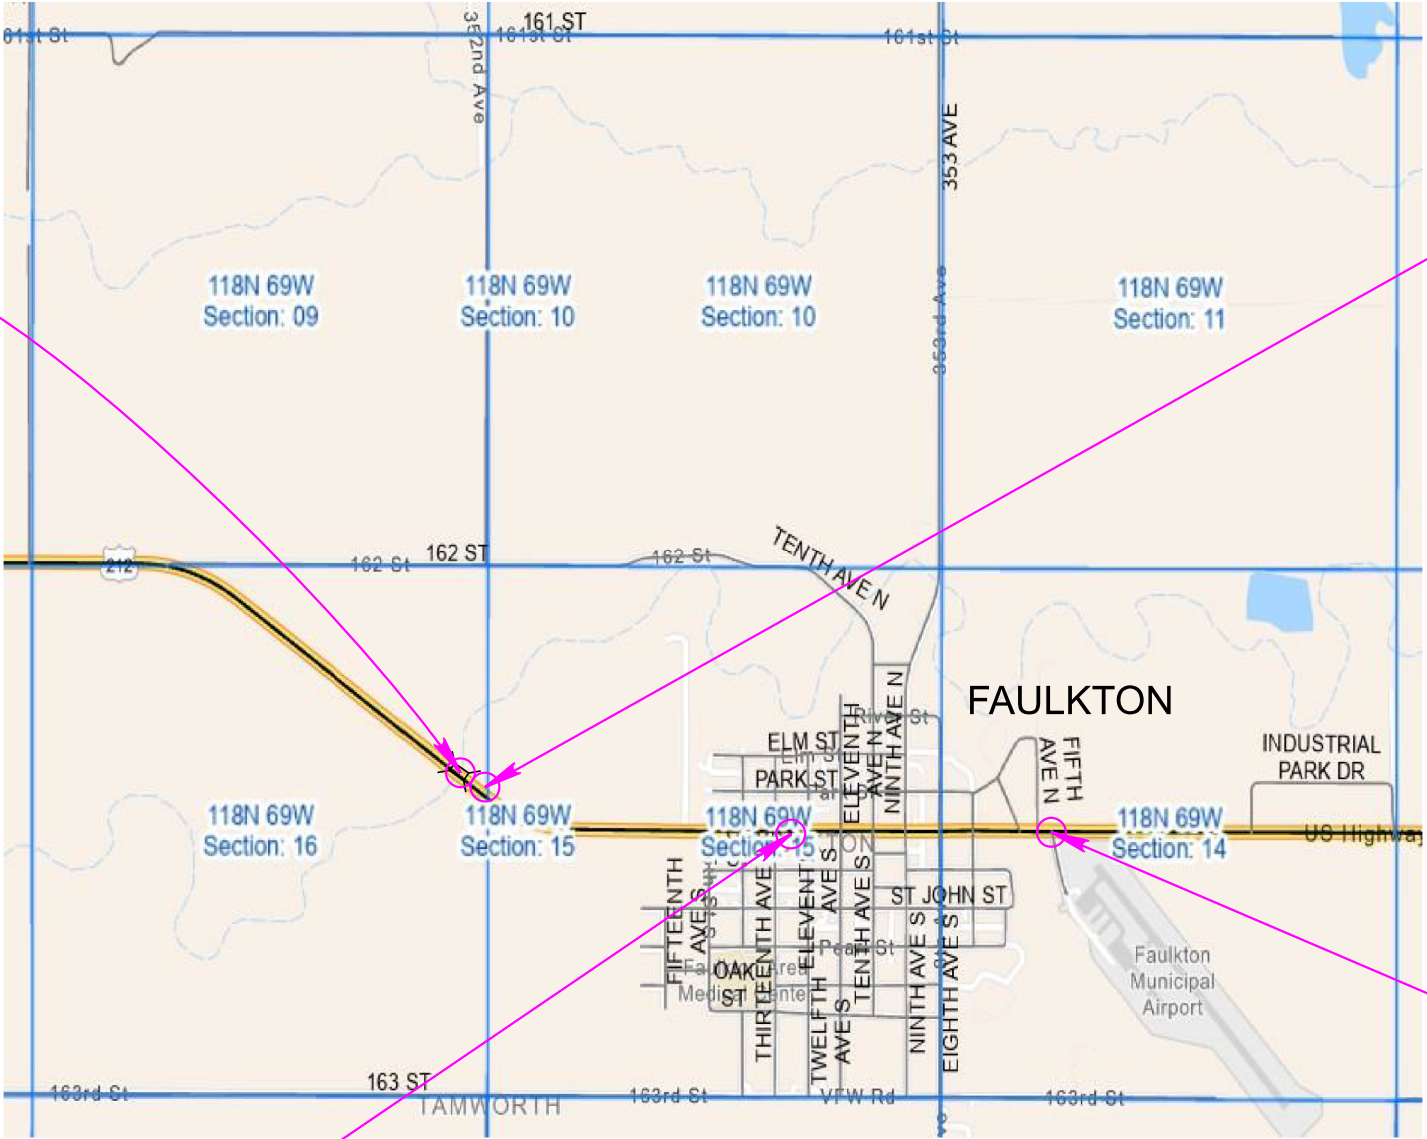

SECTION D ESTIMATE OF QUANTITIES

BID ITEM NUMBER	ITEM	QUANTITY	UNIT
110E1690	Remove Sediment	4.8	CuYd
110E1693	Remove Erosion Control Wattle	155	Ft
110E1695	Remove Sediment Filter Bag	12	Ft
110E1700	Remove Silt Fence	194	Ft
230E0010	Placing Topsoil	1,298	CuYd
730E0100	Cover Crop Seeding	2.5	Bu
730E0206	Type D Permanent Seed Mixture	1	Lb
730E0212	Type G Permanent Seed Mixture	63	Lb
731E0200	Fertilizing	1.20	Ton
732E0100	Mulching	4.9	Ton
732E0500	Fiber Reinforced Matrix	1.2	Ton
734E0044	Soil Stabilizer	1.5	Acre
734E0101	Type 1 Erosion Control Blanket	13	SqYd
734E0103	Type 3 Erosion Control Blanket	100	SqYd
734E0154	12" Diameter Erosion Control Wattle	620	Ft
734E0165	Remove and Reset Erosion Control Wattle	194	Ft
734E0180	Sediment Filter Bag	48	Ft
734E0325	Surface Roughening	1.5	Acre
734E0602	Low Flow Silt Fence	740	Ft
734E0604	High Flow Silt Fence	136	Ft
734E0610	Mucking Silt Fence	54	CuYd
734E0620	Repair Silt Fence	194	Ft
734E0845	Sediment Control at Inlet with Frame and Grate	3	Each
900E1320	Construction Entrance	1	Each

PLACING TOPSOIL

The thickness will be approximately 4 inches within the right-of-way and 6 inches on temporary easements.

The estimated amount of topsoil to be placed is as follows:

Station	to	Station	Topsoil (CuYd)
1114+59		1123+26	1,297
1160+00		1165+37	1
Total:			1,298

COVER CROP SEEDING

Cover crop seeding may be used on this project as a temporary erosion control measure. The actual limits and use of cover crop seeding will be determined by the Engineer during construction.

MYCORRHIZAL INOCULUM

Mycorrhizal inoculum will consist of mycorrhizal fungi spores and mycorrhizal fungi-infected root fragments in a solid carrier. The carrier may include organic materials, calcinated clay, or other materials consistent with application and good plant growth. The supplier will provide certification of the fungal species claimed and the live propagule count. The inoculum will include a minimum 25% the fungal species *Rhizophagus intraradices*. The remaining 75% may include other endomycorrhizal fungal species.

For all Type D Permanent Seed, the seed will be inoculated by the seed supplier with a minimum of 20,000 live propagules of mycorrhizal fungi per 1,000 square feet. All costs of inoculating the seed will be incidental to the contract unit price per pound for the corresponding permanent seed mixture.

For all Type G Permanent Seed, the seed will be inoculated by the seed supplier with a minimum of 100,000 live propagules of mycorrhizal fungi per acre. All costs of inoculating the seed will be incidental to the contract unit price per pound for the corresponding permanent seed mixture.

The Mycorrhizal Inoculum provided will be from the approved product list. The approved product list may be viewed at the following internet site:

<https://apps.sd.gov/HC60ApprovedProducts/main.aspx>

FERTILIZING

The Contractor will apply an all-natural slow-release fertilizer prior to seeding or placing sod. The all-natural fertilizer will have a minimum guaranteed analysis of 4-4-4 and be USDA Certified BioBased. It should provide a minimum of 4% (N) nitrogen with a minimum water insoluble nitrogen (WIN) fraction of 2.07%, a minimum of 4% (P2O5) available phosphate, a minimum of 4% (K2O) soluble potash, and a maximum carbon to nitrogen ratio (C:N ratio) of 5:1. The all-natural fertilizer will be free of weed-seed and pathogens accomplished through thermophilic composting, and not mechanical or chemical sterilization, to assure presence of beneficial soil microbiology. The fertilizer will have a near neutral pH, a low salt index, a low biological oxygen demand, contain organic humic and fulvic acids, and have high aerobic organism counts. The fertilizer will also be stable, free of bad odors, and be unattractive as a food source for animals. It should also be in a granular form that is easily spread.

For all Type D Permanent Seed, fertilizer will be applied at a rate of 34 pounds per 1,000 SqFt and in accordance with the manufacturer's recommended method of application.

For all Type G Permanent Seed, fertilizer will be applied at a rate of 1,000 pounds per acre and in accordance with the manufacturer's recommended method of application.

The all-natural slow release fertilizer will be as shown below or an approved equal:

<https://apps.sd.gov/HC60ApprovedProducts/main.aspx>

 Plotting Date: 06/22/2026	PROJECT	SECTION	SHEET
	NH-B 0212(194)266	D2	D19

PERMANENT SEEDING

The areas to be seeded consist of all newly graded areas within the project limits except for the top of roadways and temporary easements under cultivation.

Lawn and turf seed, such as the Type D Permanent Seed Mixture, will be tested within 12 months prior to planting, exclusive of the calendar month in which the test was completed.

Type D Permanent Seed Mixture is to be used for all revegetation between 1164+00 to 1165+37.

Type D Permanent Seed Mixture will consist of the following:

Grass Species	Variety	Pure Live Seed (PLS) (Pounds/1000 SqFt)
Kentucky Bluegrass	Avalanche, Appalachian, Wildhorse, Blue Bonnet, Action	1.4
Perennial Ryegrass	Turf Type Varieties	1.4
Creeping Red Fescue	Epic, Boreal, Chantilly	1.4
Chewings Fescue	Ambrose, K2, Zodiac, Shadow III	1.4
Alkali Grass	Fults, Fults II, Quill, Salty	1.4
Total:		7

Type G Permanent Seed Mixture will consist of the following:

Grass Species	Variety	Pure Live Seed (PLS) (Pounds/Acre)
Western Wheatgrass	Arriba, Flintlock, Rodan, Rosana, Walsh	7
Switchgrass	Dacotah, Forestburg, Nebraska 28, Pathfinder, Summer, Sunburst, Trailblazer	3
Indiangrass	Holt, Tomahawk, Chief, Nebraska 54	3
Big Bluestem	Bison, Bonilla, Champ, Sunnyview, Rountree, Bonanza	3
Oats or Spring Wheat: April through May; Winter Wheat: August through November		10
Total:		26

SURFACE ROUGHENING

Surface roughening will be done after topsoil placement and before permanent seeding, fertilizing, and mulching applications. Refer to Standard Plate 734.25 for details.

TABLE OF SURFACE ROUGHENING

Station	Location	Area (Acre)
1117+50 to 1120+50 L/R	Disturbed area	0.4
5+60 to 7+25 L/R (Diversion)	Disturbed area	0.1
	Additional Quantity:	1.0
	Total:	1.5

MULCHING (GRASS HAY OR STRAW)

If the Contractor uses a no-till drill, mulch may be applied prior to seeding and the mulch can then be punched into the soil by the no-till drill. If the Contractor uses this process, the no-till drill seeding will be completed immediately following the mulch application and the mulch will be punched into the soil at a 3-inch depth.

An additional 1 ton of Grass Hay or Straw Mulch has been added to the Estimate of Quantities for temporary erosion control on areas determined by the Engineer during construction.

FIBER REINFORCED MATRIX

Fiber reinforced matrix will be applied in a separate operation following permanent seeding at locations noted in the table and at locations determined by the Engineer during construction. The application rate is 3,000 pounds per acre.

An additional quantity of Fiber Reinforced Matrix has been added to the Estimate of Quantities for erosion control on areas determined by the Engineer during construction.

The Contractor will use a Fiber Reinforced Matrix from the approved products list, or an approved equal. The approved product list for Fiber Reinforced Matrix may be viewed at the following internet site.

<https://apps.sd.gov/HC60ApprovedProducts/main.aspx>

TABLE OF FIBER REINFORCED MATRIX

Station	Location	Quantity (Ton)
1117+50 to 1120+50 L/R	Inslope/Backslope	0.7
	Additional Quantity:	0.5
	Total:	1.2

SOIL STABILIZER

Soil stabilizer will be applied on the areas listed in the table and any other areas deemed necessary by the Engineer. The soil stabilizer limits will be adjusted as necessary by the Engineer during construction.

An estimated quantity of 1 acre of soil stabilizer has been included in the Estimate of Quantities. The soil stabilizer will be applied on permanently seeded areas and areas deemed necessary by the Engineer.

The Contractor will apply soil stabilizer in accordance with the manufacturer's application instructions and at the rate specified in the list of approved soil stabilizers.

Wood fiber mulch that contains a green dye will be mixed with the soil stabilizer to be used as a tracer when the soil stabilizer is applied hydraulically. Wood fiber mulch will be added at a rate of 300 pounds per acre to all of the approved soil stabilizers listed in the table except for the Pam-12 Plus product. The wood fiber mulch will be a 100% wood fiber product and does not need to contain a tackifier.

All costs for furnishing and applying the soil stabilizer including wood fiber mulch, hauling, materials, equipment, labor, and incidentals necessary will be paid for at the contract unit price per Acre for "Soil Stabilizer".

The Soil Stabilizer provided will be from the approved product list. The approved product list may be viewed at the following internet site:

<https://apps.sd.gov/HC60ApprovedProducts/main.aspx>

TABLE OF SOIL STABILIZER

Station	Location	Quantity (Acre)
1117+50 to 1120+50 L/R	Disturbed area	0.4
5+60 to 7+25 L/R (Diversion)	Disturbed area	0.1
	Additional Quantity:	1.0
	Total:	1.5

EROSION CONTROL WATTLE

Erosion control wattles for restraining the flow of runoff and sediment will be installed at locations noted in the table and at locations determined by the Engineer during construction. Refer to Standard Plate 734.06 for details.

The Contractor will provide certification that the erosion control wattles do not contain noxious weed seeds.

Erosion control wattles will remain on the project to decompose.

An additional quantity of 12" Diameter Erosion Control Wattles has been added to the Estimate of Quantities for temporary erosion and sediment control in highway ditch channels and as an alternative to low flow or high flow silt fence at wetland areas adjacent to the highway.

The erosion control wattle provided will be from the approved product list. The approved product list for erosion control wattle may be viewed at the following internet site:

<https://apps.sd.gov/HC60ApprovedProducts/main.aspx>



Plotting Date: 06/22/2026

PROJECT		SECTION	SHEET
NH-B 0212(194)266		D3	D19

TABLE OF EROSION CONTROL WATTLE

Station	Location	Quantity (Ft)
1118+00 to 1118+70 L	Toe of slope	95
1118+00 to 1118+70 R	Toe of slope	80
1119+00 to 1120+60 R	Toe of slope	125
1119+50 to 1120+60 L	Toe of slope	120
	Additional Quantity:	200
	Total:	620

LOW FLOW SILT FENCE

The low flow silt fence fabric provided will be from the approved product list. The approved product list for low flow silt fence may be viewed at the following internet site:

<https://apps.sd.gov/HC60ApprovedProducts/main.aspx>

Low flow silt fence will be placed at the locations noted in the table and at locations that will minimize siltation of adjacent streams, lakes, dams, or drainage areas as determined by the Engineer during construction. Refer to Standard Plate 734.04 for details.

An additional quantity of Low Flow Silt Fence has been added to the Estimate of Quantities for temporary sediment control.

TABLE OF LOW FLOW SILT FENCE

Station	Location	Quantity (Ft)
1117+50 to 1118+70 L	Perimeter control	150
5+40 to 6+15 R (Diversion)	Perimeter control	100
6+60 to 7+25 R (Diversion)	Perimeter control	85
1119+50 to 1120+75 L	Perimeter control	155
	Additional Quantity:	250
	Total:	740

HIGH FLOW SILT FENCE

The high flow silt fence fabric provided will be from the approved product list. The approved product list for high flow silt fence may be viewed at the following internet site:

<https://apps.sd.gov/HC60ApprovedProducts/main.aspx>

High flow silt fence will be placed at the locations noted in the table and at locations that will minimize siltation of adjacent streams, lakes, dams, or drainage areas as determined by the Engineer during construction. Refer to Standard Plate 734.05 for details.

An additional quantity of high flow silt fence has been added to the Estimate of Quantities for temporary sediment control.

TABLE OF HIGH FLOW SILT FENCE

Station	Location	Quantity (Ft)
	Quantity from Interim Sediment Control at Inlets:	36
	Additional Quantity:	100
	Total:	136

EROSION CONTROL BLANKET

Erosion control blanket will be installed 16 feet wide at the locations noted in the table and at locations determined by the Engineer during construction.

The erosion control blanket provided will be from the approved product list. The approved product list for erosion control blanket may be viewed at the following internet site:

<https://apps.sd.gov/HC60ApprovedProducts/main.aspx>

An additional quantity of Type 3 Erosion Control Blanket has been added to the Estimate of Quantities for temporary erosion control.

TABLE OF EROSION CONTROL BLANKET

Station	Location	Type	Quantity (SqYd)
1163+65 R	Between ramps	1	13
	Additional Quantity:	3	100
	Total Type 1 Erosion Control Blanket:		13
	Total Type 3 Erosion Control Blanket:		100

INTERIM SEDIMENT CONTROL AT INLETS, MANHOLES, AND JUNCTION BOXES AFTER SURFACING REMOVAL AND BEFORE PLACEMENT OF SURFACING

Refer to Standard Plate 734.05 for details of installation of high flow silt fence at drop inlets, manholes, and junction boxes.

The high flow silt fence fabric provided will be from the approved product list. The approved product list for high flow silt fence may be viewed at the following internet site:

<https://apps.sd.gov/HC60ApprovedProducts/main.aspx>

In addition, the Contractor will do the following for this installation:

- A space of at least 1’ will be provided between the silt fence installation and the inlet. This space will be filled completely with a 2” depth of aggregate, 2” minus or smaller.
- The top elevation of the silt fence will be such that a 12” horizontal flap of silt fence will remain at the bottom.
- The base of the silt fence will conform to the natural ground profile but does not need to be trenched in at the bottom.
- The extra 12” of the silt fence material may be cut so that the material will lay flat upon the subgrade.
- Sediment filter bags will be placed on the 12” flap around the perimeter of the silt fence installation. The sediment filter bags will overlap 6” at the ends and be placed tightly together.
- The sediment filter bags will be filled with clean aggregate 2” minus or smaller.

The Sediment Filter Bag provided will be from the approved product list. The approved product list may be viewed at the following internet site:

<https://apps.sd.gov/HC60ApprovedProducts/main.aspx>

All costs for furnishing and installing the sediment filter bags will be incidental to the contract unit price per foot for “Sediment Filter Bag.”

All costs for removing the sediment filter bags will be incidental to the contract unit price per foot for “Remove Sediment Filter Bag”.

Payment for high flow silt fence will be as stated in Section 734.5 of the Specifications.

All costs for furnishing, installing, and removing the 2” depth of aggregate will be incidental to other erosion and sediment control contract items.

All costs for removing and disposing of sediment collected by the sediment control device will be incidental to the contract unit price per cubic yard for “Remove Sediment”.

The removed sediment will be placed at a location away from the drop inlet where the sediment will not be washed back into the drop inlet or other storm sewer system.

The Contractor and Engineer will inspect and maintain the sediment control device once every week and within 24 hours after every rainfall event greater than 1/2”.



Plotting Date: 06/22/2026

PROJECT	SECTION	SHEET
NH-B 0212(194)266	D4	D19

TABLE OF INTERIM SEDIMENT CONTROL AT INLETS, MANHOLES, AND JUNCTION BOXES AFTER SURFACING REMOVAL AND BEFORE PLACEMENT OF SURFACING

Station	High Flow Silt Fence Quantity (Ft)	Sediment Filter Bag Quantity (Ft)	Remove Sediment Quantity (CuYd)
1119+58 L	18	24	0.25
1119+58 R	18	24	0.25
Totals:	36	48	0.50

SEDIMENT CONTROL AT INLETS WITH FRAMES AND GRATES

This type of sediment control device should be used where there is pavement in the vicinity of the drop inlets and stormwater or sediment could possibly enter the frame and grate. Sediment Control at Inlet with Frame and Grate will be installed prior to working in the vicinity of the drop inlets.

The Contractor will be responsible for maintaining and repairing the sediment control devices for the duration of the project for which sediment control measures are required. Maintenance will be scheduled to prevent storm water from backing up into the driving lane.

“Sediment Control at Inlet with Frame and Grate” will be paid for one time at each location, regardless of the number of times the sediment control devices are installed, inspected, cleaned, removed, repaired, or replaced. All costs associated with furnishing, installing, inspecting, maintaining, cleaning, sediment removal, and repairing Sediment Control at Inlet with Frame and Grate will be incidental to the contract unit price per each for “Sediment Control at Inlet with Frame and Grate”.

The Sediment Control at Inlets with Frames and Grates provided will be from the approved product list. The approved product list may be viewed at the following internet site:

<https://apps.sd.gov/HC60ApprovedProducts/main.aspx>

TABLE OF SEDIMENT CONTROL AT INLETS WITH FRAMES AND GRATES

Station	Quantity (Each)
1119+58 L	1
1119+58 R	1
1163+54 R	1
Total:	3

DEWATERING AND SEDIMENT COLLECTING

The Contactor has the option to treat sediment laden water trapped within the project limits or the Contractor may elect to transport sediment laden water off the project. Refer to the OPTIONS FOR DEWATERING AND SEDIMENT COLLECTING detail sheet for more information.

Water transported off the project limits will not be disposed of in an area where it can enter a waterway. The disposal site must be approved by the Engineer.

The Dewatering and Sediment Control products provided will be from the from the approved products list. The approved products list may be viewed on the Dewatering and Sediment Collection Standard Plate, or at the following internet site:

<https://apps.sd.gov/HC60ApprovedProducts/main.aspx>

Separate payment will not be made for any Dewatering and Sediment Collection efforts. All costs involved with necessary Dewatering and Sediment Collection efforts will be incidental to other contract items

CONSTRUCTION ENTRANCE

The Contractor will install a Construction Entrance at locations where there is a potential for mud tracking and sediment flow from the construction site and work area onto a paved public roadway.

It is the Contractor's option to use the SDDOT Construction Entrance (See SDDOT Construction Entrance notes and details), a product from the list provided in these notes, or other products or processes as approved by the Engineer during construction.

If the Contractor elects to use one of the products listed in the table, then the Contractor will install the construction entrance product in accordance with the manufacturer's installation instructions or as directed by the Engineer.

The Contractor will maintain the construction entrance such that mud tracking and sediment flow will not enter the roadway or adjacent drainage areas. The construction entrance will be routinely inspected, and the Contractor will repair or replace material as deemed necessary by the Engineer.

The Construction Entrance provided will be from the approved product list. The approved product list may be viewed at the following internet site:

<https://apps.sd.gov/HC60ApprovedProducts/main.aspx>

All costs for furnishing, installing, maintaining, and removal of the construction entrance including equipment, labor, materials, and incidentals will be included in the contract unit price per each for "Construction Entrance".

SDDOT CONSTRUCTION ENTRANCE

If the SDDOT Construction Entrance is utilized, then the Contractor will install the SDDOT Construction Entrance in accordance with these notes and the detail drawings.

Pit run material will be obtained from a granular source and will conform to the following gradation:

Sieve Size	Percent Passing
6"	100%
#4	0-60%
#200	0-20%

The pit run material will be compacted to the satisfaction of the Engineer.

The aggregate for the granular material will conform to the following gradation requirements:

Sieve Size	Percent Passing
3"	100%
2 1/2"	90-100%
1 1/2"	25-60%
3/4"	0-10%
1/2"	0-5%

The granular material will be placed in 6" maximum lifts.

It is anticipated that the granular material will need to be periodically removed and replaced as it becomes inundated with mud and sediment.

The Reinforcement Fabric (MSE) will be in conformance with Section 831 of the Specifications. The Reinforcement Fabric (MSE) will be on the Approved Products List for this material or will be certified by the supplier to meet this specification prior to installation.

The Reinforcement Fabric (MSE) should be kept as taut as possible prior to placing.

Equipment will not be allowed on the Reinforcement Fabric (MSE) until the first lift of granular material is in place.

All seams in the Reinforcement Fabric (MSE) will be overlapped at least 2' and shingled.



Plotting Date: 06/22/2026

PROJECT	SECTION	SHEET
NH-B 0212(194)266	D5	D19

VEGETATED BUFFER STRIPS

Vegetated Buffer Strips are sections of existing undisturbed vegetation adjacent to disturbed areas and are meant to convey sheet flow runoff from disturbed areas, resulting in the trapping of sediment and other pollutants as the runoff passes through vegetation and infiltration occurs.

Vegetated Buffer Strips should be utilized along existing floodplains, wetlands, channels, and other bodies of water, whenever possible. They are also useful at any areas where runoff may leave the site. Vegetated Buffer Strips should be a minimum of 15' wide and perpendicular to flow. Vegetated Buffer Strips will be installed at locations determined by the Engineer during construction.

Separate payment will not be made for Vegetated Buffer Strips.

STORMWATER POLLUTION PREVENTION PLAN CHECKLIST
*(The numbers left of the title headings are **reference numbers** to the **GENERAL PERMIT FOR STORM WATER DISCHARGES ASSOCIATED WITH CONSTRUCTION ACTIVITIES** (Stormwater Permit))*

5.3 (2): STAFF TRAINING/SWPPP IMPLEMENTATION

To promote stormwater management awareness specific for this project, the Contractor's Erosion Control Supervisor should provide correspondence of how the SWPPP will be implemented. The Contractor's Erosion Control Supervisor is responsible for providing this information at the preconstruction meeting, and subsequently completing an attendance log, which should identify site-specific implementation of the SWPPP and the names of the personnel who attended the preconstruction meeting. Documentation of the preconstruction meeting will be filed with the SWPPP documents.

5.3 (3): DESCRIPTION OF CONSTRUCTION ACTIVITIES

- **5.3 (3a): Project Limits** (See Title Sheet)
- **5.3 (3a): Project Description** (See Title Sheet)
- **5.3 (4): Site Map(s)** (See Title Sheet and Plans)
- **Major Soil Disturbing Activities** (check all that apply)
 - ☒ Clearing and grubbing
 - ☒ Excavation/borrow
 - ☒ Grading and shaping
 - ☐ Filling
 - ☐ Other (describe):
- **5.3 (3b): Total Project Area** 6 Acres
- **5.3 (3b): Total Area to be Disturbed** 4 Acres
- **5.3 (3c): Maximum Area Disturbed at One Time**
- **5.3 (3d): Existing Vegetative Cover** 65%
- **5.3 (3d): Description of Vegetative Cover** Typical East River native and introduced roadside vegetation
- **5.3 (3e): Soil Properties:** Loams
- **5.3 (3f): Name of Receiving Water Body/Bodies** South Fork Snake Creek
- **5.3 (3g): Location of Construction Support Activity Areas**

5.3 (3h): ORDER OF CONSTRUCTION ACTIVITIES

- **Special sequencing requirements** (see Section C).
The Contractor will enter the Estimated Start Date.

Description	Estimated Start Date
Install stabilized construction entrance(s).	
Install perimeter protection where runoff may exit site.	
Install perimeter protection around stockpiles.	
Install channel and ditch bottom protection.	
Clearing and grubbing.	
Remove and stockpile topsoil.	
Stabilize disturbed areas.	
Install utilities, storm sewers, curb and gutter.	
Install inlet and culvert protection after completing storm drainage and other utility installations.	
Final grading.	
Final paving.	
Removal of protection devices.	
Reseed areas disturbed by removal activities.	

5.3 (5): DESCRIPTION AND MAINTENANCE OF CONTROL MEASURES

All controls will be maintained in good working order. Necessary repairs will be initiated within 24 hours of the site inspection report. Include the technical reasoning for selecting each control. (Check all that apply)

Perimeter Controls (See Detail Plan Sheets)	
Description	Estimated Start Date
☒ Natural Buffers (within 50 ft of Waters of State)	
☒ Silt Fence	
☒ Erosion Control Wattles	
☐ Temporary Berm / Windrow	
☐ Floating Silt Curtain	
☐ Stabilized Construction Entrances	
☐ Entrance/Exit Equipment Tire Wash	
☐ Other:	

Structural Erosion and Sediment Controls	
Description	Estimated Start Date
☒ Silt Fence	
☐ Temporary Berm/Windrow	
☐ Erosion Control Wattles	
☐ Temporary Sediment Barriers	
☐ Erosion Bales	
☐ Temporary Slope Drain	
☐ Turf Reinforcement Mat	
☐ Riprap	
☐ Gabions	
☐ Rock Check Dams	
☐ Sediment Traps/Basins	
☐ Culvert Inlet Protection	
☐ Transition Mats	
☐ Median/Area Drain Inlet Protection	
☒ Curb Inlet Protection	
☐ Interceptor Ditch	
☐ Concrete Washout Facility	
☐ Work Platform	
☐ Temporary Water Barrier	
☐ Temporary Water Crossing	
☐ Permanent Stormwater Ponds	
☐ Permanent Open Vegetated Swales	
☐ Natural Depressions to allow for Infiltration	
☐ Sequential Systems that combine several practices	
☐ Other:	



Plotting Date: 06/22/2026

PROJECT		SECTION	SHEET
NH-B 0212(194)266		D6	D19

Dust Controls

Description	Estimated Start Date
☐ Tarps & Wind impervious fabrics	
☐ Watering	
☐ Stockpile location/orientation	
☐ Dust Control Chlorides	
☐ Other	

Dewatering BMPs

Description	Estimated Start Date
☐ Sediment Basins	
☐ Dewatering bags	
☐ Weir tanks	
☐ Temporary Diversion Channel	
☐ Other:	

Stabilization Practices (See Detail Plan Sheets)

(Stabilization measures will begin the following work day whenever earth disturbing activity on any portion of the site has temporarily or permanently ceased. Temporary stabilization will be completed as soon as practicable but no later than 14 days after initiating soil stabilization activities (**3.18**))

Description	Estimated Start Date
☐ Vegetation Buffer Strips	
☒ Temporary Seeding (Cover Crop Seeding)	
☒ Permanent Seeding	
☐ Sodding	
☐ Planting (Woody Vegetation for Soil Stabilization)	
☒ Mulching (Grass Hay or Straw)	
☐ Fiber Mulching (Wood Fiber Mulch)	
☒ Soil Stabilizer	
☐ Bonded Fiber Matrix	
☒ Fiber Reinforced Matrix	
☒ Erosion Control Blankets	
☒ Surface Roughening (e.g. tracking)	
☐ Other:	

Wetland Avoidance

Will construction and/or erosion and sediment controls impinge on regulated wetlands? Yes ☒ No ☐ If yes, the structural and erosion and sediment controls have been included in the total project wetland impacts and have been included in the 404 permit process with the USACE.

5.3 (6): PROCEDURES FOR INSPECTIONS

- Inspections will be conducted at least once every 7 days.
- All controls will be maintained in good working order. Necessary repairs will be initiated within 24 hours of the site inspection report.
- Silt fence will be inspected for depth of sediment and for tears to ensure the fabric is securely attached to the posts and that the posts are well anchored. Sediment buildup will be removed from the silt fence when it reaches 1/3 of the height of the silt fence.
- Sediment basins and traps will be checked. Sediment will be removed when depth reaches approximately 50 percent of the structure’s capacity, and at the conclusion of the construction.
- Check dams will be inspected for stability. Sediment will be removed when depth reaches 1/2 the height of the dam.
- All seeded areas will be checked for bare spots, washouts, and vigorous growth free of significant weed infestations.
- Inspection and maintenance reports will be prepared on form DOT 298 for each site inspection, this form will also be used to document changes to the SWPPP. A copy of the completed inspection form will be filed with the SWPPP documents.
- The SDDOT Project Engineer and Contractor’s Erosion Control Supervisor are responsible for inspections. Maintenance and repair activities are the responsibility of the Contractor. The SDDOT Project Engineer will complete the inspection and maintenance reports and distribute copies per the distribution instructions on DOT 298.

5.3 (7): POST CONSTRUCTION STORMWATER MANAGEMENT

Stormwater management will be handled by temporary controls outlined in “DESCRIPTION AND MAINTENANCE OF CONTROL MEASURES” above, and any permanent controls needed to meet permanent stormwater management needs in the post construction period will be shown in the plans and noted as permanent.

5.3 (8): POLLUTION PREVENTION PROCEDURES

5.3 (8a): Spill Prevention and Response Procedures

- **Material Management**
 - Housekeeping
 - Only needed products will be stored on-site by the Contractor.
 - Except for bulk materials the contractor will store all materials under cover and/or in appropriate containers.
 - Products must be stored in original containers and labeled.
 - Material mixing will be conducted in accordance with the manufacturer’s recommendations.
 - When possible, all products will be completely used before properly disposing of the container off-site.
 - The manufacturer’s directions for disposal of materials and containers will be followed.
 - The Contractor’s site superintendent will inspect materials storage areas regularly to ensure proper use and disposal.
 - Dust generated will be controlled in an environmentally safe manner.
 - Hazardous Materials
 - Products will be kept in original containers unless the container is not resealable and provide secondary containment as applicable.
 - Original labels and material safety data sheets will be retained in a safe place to relay important product information.
 - If surplus product must be disposed of, manufacturer’s label directions for disposal will be followed.

- Maintenance and repair of all equipment and vehicles involving oil changes, hydraulic system drain down, de-greasing operations, fuel tank drain down and removal, and other activities which may result in the accidental release of contaminants will be conducted on an impervious surface and under cover during wet weather to prevent the release of contaminants onto the ground.
- Wheel wash water will be collected and allowed to settle out suspended solids prior to discharge. Wheel wash water will not be discharged directly into any stormwater system or stormwater treatment system.
- Potential pH-modifying materials such as: bulk cement, cement kiln dust, fly ash, new concrete washings, concrete pumping, residuals from concrete saw cutting (either wet or dry), and mixer washout waters will be collected on site and managed to prevent contamination of stormwater runoff.

➤ **Spill Control Practices**

In addition to the previous housekeeping and management practices, the following practices will be followed for spill prevention and cleanup if needed.

- For all hazardous materials stored on site, the manufacturer’s recommended methods for spill cleanup will be clearly posted. Site personnel will be made aware of the procedures and the locations of the information and cleanup supplies.
- Appropriate cleanup materials and equipment will be maintained by the Contractor in the materials storage area on-site. As appropriate, equipment and materials may include items such as brooms, dust pans, mops, rags, gloves, goggles, kitty litter, sand, sawdust, and plastic and metal trash containers specifically for cleanup purposes.
- All spills will be cleaned immediately after discovery and the materials disposed of properly.
- The spill area will be kept well ventilated and personnel will wear appropriate protective clothing to prevent injury from contact with a hazardous substance.
- After a spill a report will be prepared describing the spill, what caused it, and the cleanup measures taken. The spill prevention plan will be adjusted to include measures to prevent this type of spill from reoccurring, as well as clean up instructions in the event of reoccurrences.
- The Contractor’s site superintendent, responsible for day-to-day operations, will be the spill prevention and cleanup coordinator.

➤ **Spill Response**

The primary objective in responding to a spill is to quickly contain the material(s) and prevent or minimize migration into stormwater runoff and conveyance systems. If the release has impacted on-site stormwater, it is critical to contain the released materials on-site and prevent their release into receiving waters. If a spill of pollutants threatens stormwater or surface water at the site, the spill response procedures outlined below must be implemented in a timely manner to prevent the release of pollutants.

- The Contractor’s site superintendent will be notified immediately when a spill or the threat of a spill is observed. The superintendent will assess the situation and determine the appropriate response.
- If spills represent an imminent threat of escaping erosion and sediment controls and entering receiving waters, personnel will be directed to respond immediately to contain the release and notify the superintendent after the situation has been stabilized.

- Spill kits containing appropriate materials and equipment for spill response and cleanup will be maintained by the Contractor at the site.
- If oil sheen is observed on surface water (e.g. settling ponds, detention ponds, swales), action will be taken immediately to remove the material causing the sheen. The Contractor will use appropriate materials to contain and absorb the spill. The source of the oil sheen will also be identified and removed or repaired as necessary to prevent further releases.
- If a spill occurs the superintendent or the superintendent’s designee will be responsible for completing the spill reporting form and for reporting the spill to SDDANR.
- Personnel with primary responsibility for spill response and cleanup will receive training by the Contractor’s site superintendent or designee. The training must include identifying the location of the spill kits and other spill response equipment and the use of spill response materials.
- Spill response equipment will be inspected and maintained as necessary to replace any materials used in spill response activities.

5.3 (8b): WASTE MANAGEMENT PROCEDURES

➤ **Waste Disposal**

- All liquid waste materials will be collected and stored in approved sealed containers. All trash and construction debris from the site will be deposited in the approved containers. Containers will be serviced as necessary, and the trash will be hauled to an approved disposal site or licensed landfill. All onsite personnel will be instructed in the proper procedures for waste disposal and notices stating proper practices will be posted. The Contractor is responsible for ensuring waste disposal procedures are followed.

➤ **Hazardous Waste**

- All hazardous waste materials will be disposed of in a manner specified by local or state regulations or by the manufacturer. Site personnel will be instructed in these practices, and the Contractor will be responsible for seeing that these practices are followed.

➤ **Sanitary Waste**

- Portable sanitary facilities will be provided on all construction sites. Sanitary waste will be collected from the portable units which must be secured to prevent tipping and serviced in a timely manner by a licensed waste management Contractor or as required by any local regulations.

EROSION AND SEDIMENT CONTROL LEGEND



Plotting Date: 06/22/2026

PROJECT		SECTION	SHEET
NH-B 0212(194)266		D10	D19

- Silt Fence J-Hooks
- Low Flow Silt Fence
- High Flow Silt Fence
- High Flow Silt Fence at Pipe
- Sediment Control at Inlet After Placement of Surfacing
- Sediment Control at Inlet Before Placement of Surfacing
- Temporary Sediment Barrier
- Temporary Water Barrier
- Floating Silt Curtain
- Sediment Filter Bags
- Triangular Silt Barriers
- Erosion Control Wattles on Slopes
- Erosion Control Wattles at Inlets
- Erosion Control Wattles in Ditches
- Erosion Bales
- Surfacing Roughening
- Temporary Grass Hay or Straw Mulch/ Soil Stabilizer
- Cut Interceptor Ditch
- Temporary Slope Drain
- Soil Stabilizer/ Fiber Reinforced Matrix
- Rock Check Dam
- Type 1 Erosion Control Blanket
- Type 2 Erosion Control Blanket
- Type 3 Erosion Control Blanket
- Type 4 Erosion Control Blanket
- Type 1 Turf Reinforcement Mat
- Type 2 Turf Reinforcement Mat
- Type 3 Turf Reinforcement Mat
- Transition Mat
- Articulated Concrete Matress
- Silt Trap (See Standard Plate 734.04)
- Type D Permanant Seed Mixture

BEST MANAGEMENT PRACTICES

Best Management Practices (BMPs) are split into three categories and are to be used throughout construction.

INITIAL PHASE

BMPs from the Legend shown as Orange Symbols on the Erosion and Sediment Control Plan Sheets are to be installed in the Initial Phase prior to earth disturbing activittles and remain in place for the Intermediate Phase for temporary stabilization and in the Final Phase to achieve final stabilization.

INTERMEDIATE PHASE

BMPs from the Legend shown as Blue Symbols on the Erosion and Sediment Control Plan Sheets are to be installed in the Intermediate Phase for temporary stabilization and remain in place in the Final Phase to achieve final stabilization.

FINAL PHASE

BMPs from the Legend shown as Green Symbols on the Erosion and Sediment Control Plan Sheets are to be installed in the Final Phase to achieve final stabilization.

If these items are applicable they are to be shown in the updated SWPPP using the Symbols given.

- | | | | |
|----|---|----|--|
| TS | Topsoil Stockpile | M | On-Site Construction Material Storage Area |
| B | Borrow Area | SK | Spill Kit |
| CE | Stabilized Construction Entrance | WP | Work Platform |
| VB | Vegetated Buffer Strip | CC | Cover Crop Seeding |
| CW | Concrete Washout | PT | Portable Toilet |
| AP | Asphalt Plant Site | | |
| CP | Concrete Plant Site | | |
| V | Vehicle and Equipment Parking Area, Fueling Area, or Maintenance Area | | |
| D | Dumpster or other Trash and Debris Containers | | |

Install Low Flow Silt Fence at the following locations:
1117+50 to 1118+70 L Perimeter control 150 Ft
5+40 to 6+15 R (Diversion) 100 Ft
6+60 to 7+25 R (Diversion) 85 Ft
1119+50 to 1120+75 L Perimeter control 155 Ft

Install Interim Sediment Control at Inlets, Manholes, and Junction Boxes before the placement of surfacing at the following locations:
1119+58 - 17' L 18 Ft High Flow Silt Fence 24 Ft Sediment Filter Bags
1119+58 - 17' R 18 Ft High Flow Silt Fence 24 Ft Sediment Filter Bags

Utilize Surface Roughening at the following locations:
1117+50 to 1120+50 L/R Disturbed area 0.4 Acres
5+60 to 7+25 L/R (Diversion) Disturbed area 0.1 Acres

Apply Soil Stabilizer during active construction before topsoil placement, permanent seeding, and mulching can be completed on disturbed areas at the following locations:
1117+50 to 1120+50 L/R Disturbed area 0.4 Acres
5+60 to 7+25 L/R (Diversion) Disturbed area 0.1 Acres

Install Sediment Control at Inlets with Frames and Grates after the placement of surfacing at the following locations:
1119+58 - 17' L 1 Each
1119+58 - 17' R 1 Each

Install Type 3 Erosion Control Blanket at the following locations:
1119+58 L Pipe end 45 SqYd


Install 12" Diameter Erosion Control Wattles at the following locations:
1118+00 to 1118+70 L Toe of slope 95 Ft
1118+00 to 1118+70 R Toe of slope 80 Ft
1119+00 to 1120+60 R Toe of slope 125 Ft
1119+50 to 1120+60 L Toe of slope 120 Ft

Apply Fiber Reinforced Matrix at the following locations:
1117+50 to 1120+50 L/R Inslope/Backslope 0.7 Tons



Plotting Date: 06/22/2026

PROJECT		SECTION	SHEET
NH-B 0212(194)266		D11	D19




BEGIN DIVERSION GRADING
Station 0+00.00

BEGIN NH-B 0212(194)266
Station 1114+59.11

END DIVERSION GRADING
Station 12+69.36


END NH-B 0212(194)266
Station 1123+26.36

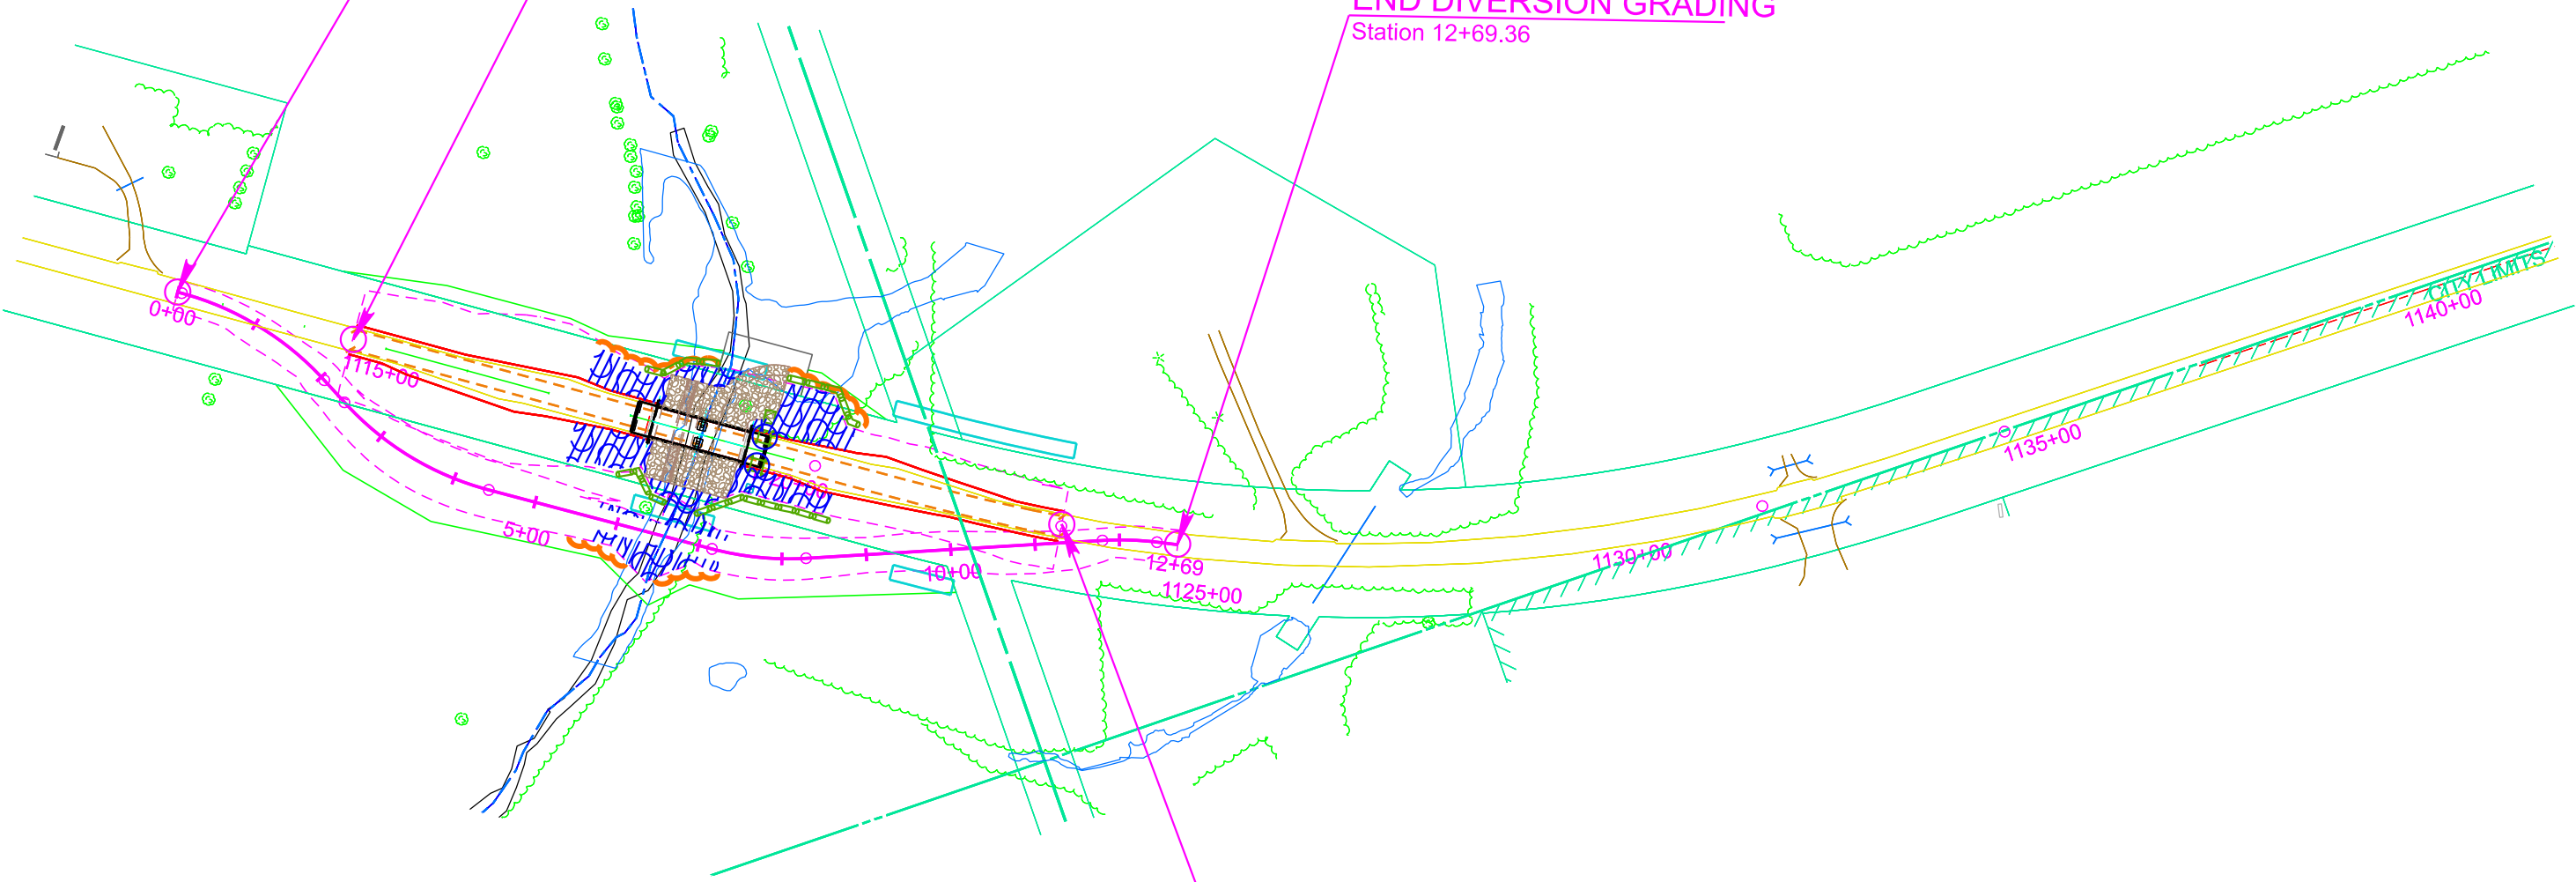

Install Sediment Control at
Inlets with Frames and Grates
after the placement of surfacing
at the following locations:
1163+54 - 26' R 1 Each

Install Type 1 Erosion Control Blanket
at the following locations:
1163+65 R Between ramps 13 SqYd

 Plotting Date: 06/22/2026	PROJECT	SECTION	SHEET
	NH-B 0212(194)266	D12	D19

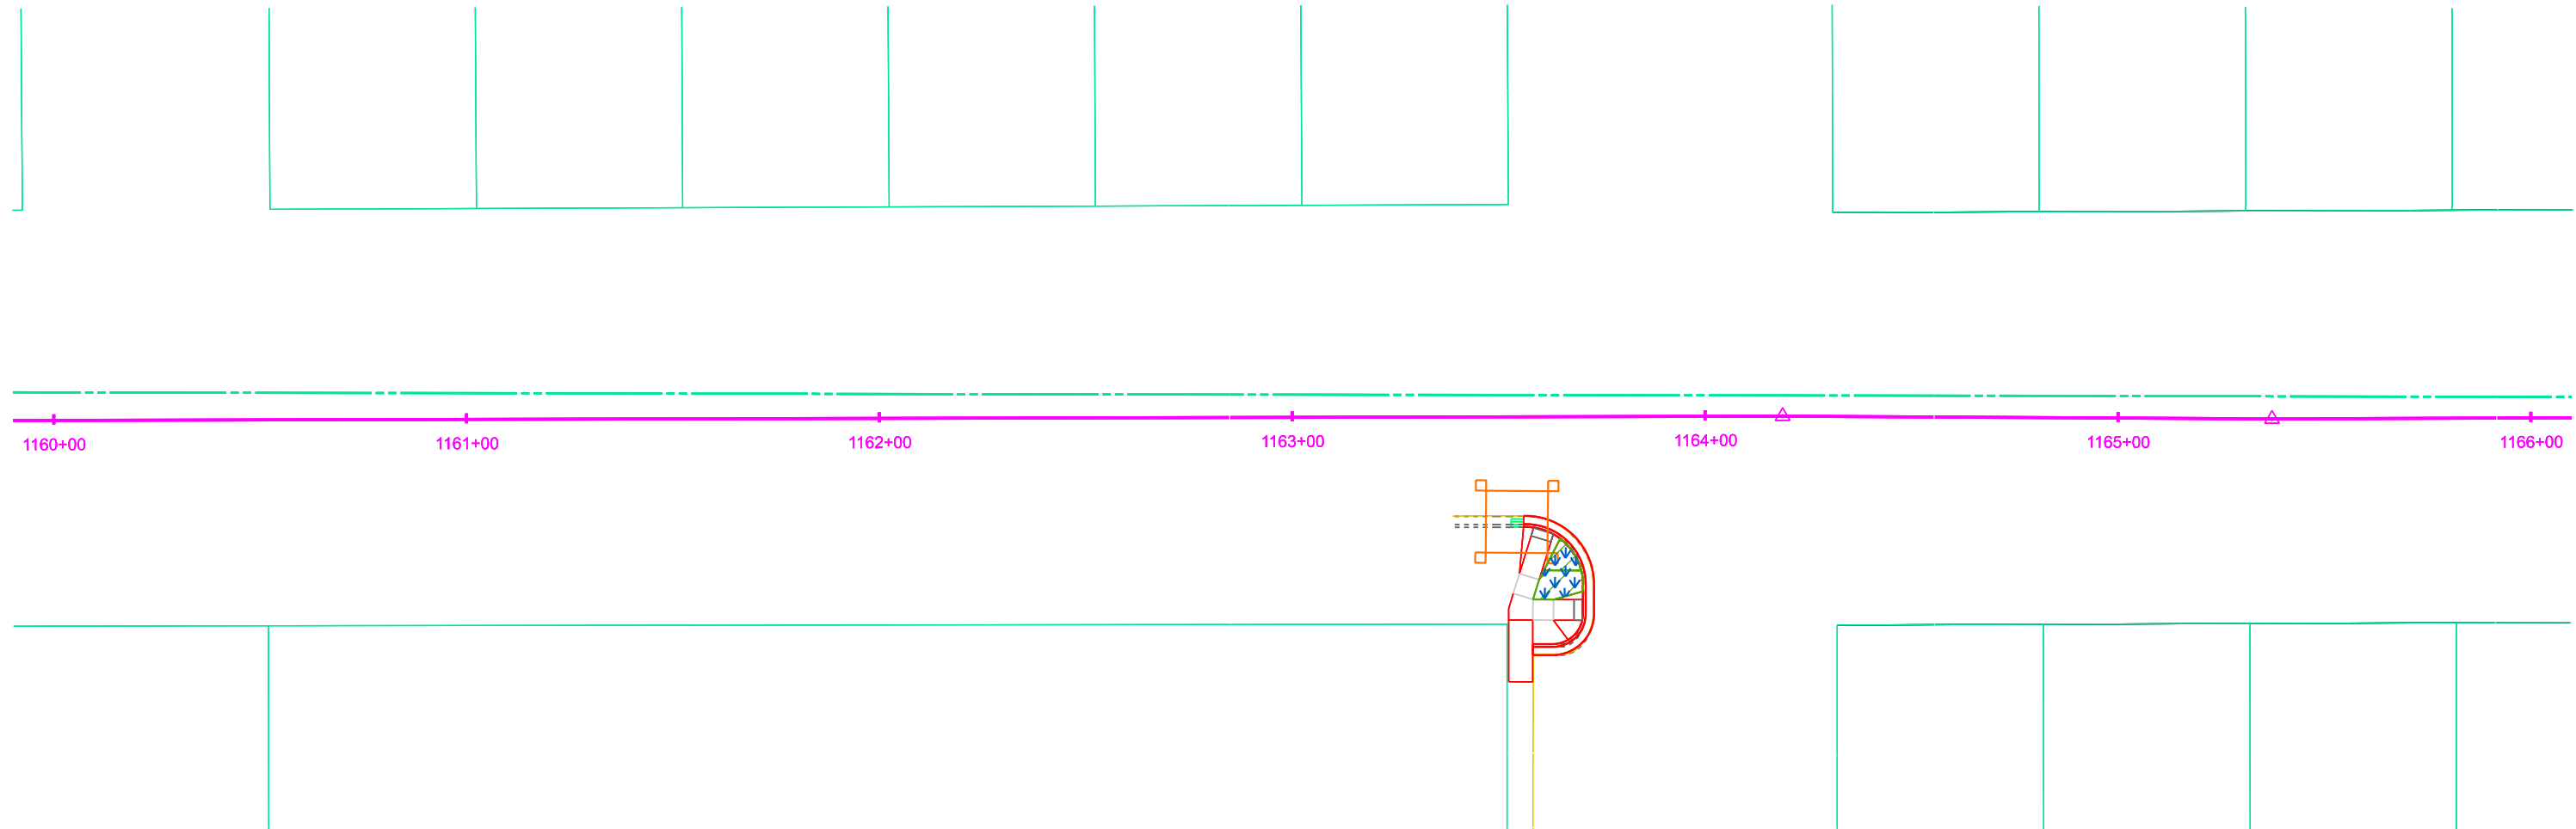

OPTIONS FOR DEWATERING AND SEDIMENT COLLECTING

 Plotting Date: 06/22/2026	PROJECT	SECTION	SHEET
	NH-B 0212(194)266	D13	D19

DEWATERING BAGS AND SOCKS capture sediment and should be placed on pavement, vegetated areas, or gravel.

Dandy Dewatering Bag
Dandy Products, Inc.
Powell, OH
Phone: 1.800.591.2284
www.dandyproducts.com

Non-woven Sediment Filter Bags
Indian Valley Industries, Inc.
Johnson City, NY
Phone: 1.800.659.5111
www.iviindustries.com

Taurus Dewatering Bags/Socks
SolHuTec Group, Inc.
Sebastian, FL
Phone: 1.888.703.9889
www.solhutech.com

Ultra-Dewatering Bag
UltraTech International, Inc
Jacksonville, FL
Phone: 1.800.764.9563
www.spillcontainment.com

Heavy Duty Dirtbag 55
ACF Environmental
Richmond, VA
Phone: 1.800.223.9021
www.acfenvironmental.com

Pump-It Tube
Flo-Water, LLC
West Des Moines, IA
Phone: 1.515.577.6763
www.flo-water.net

FLOCCULENTS listed below are considered to be safe for the environment, if used as directed:

APS 700 Series Floc Logs
Applied Polymer Systems, Inc.
Woodstock, GA
Phone: 1.866.200.9868
http://www.siltstop.com

Floc, Floc Soc, Floc Bag
Innovative Turf Solutions Products
Cincinnati, OH
Phone: 1.513.317.8311
http://www.innovativeturfsolutions.com

Biostar CH
Hild & Associates, Inc.
Stillwater, MN
Phone: 1.715.426.5131
www.biostar-ch.com

Terra-Tubes
ACF Environmental
Buffalo Grove, IL
Phone: 1.800.366.1180
www.terratubes.com

FI-3500 Tablets
JRM Chemical, Inc.
Cleveland, OH
Phone: 1.216.475.8488
http://www.soilmoist.com

Tigerfloc
Floc Systems Inc.
Surrey, British Columbia
Phone: 1.604.343.2046
www.flocsystems.com

PORTABLE FLOCCULENT SYSTEMS

Eco Pond Rescue Water Wagon
Eco Pond Rescue LLC
Seminole, Florida
Phone: 1.727.412.4323
www.ecopondrescue.com

WTS2000 Portable Sediment Tank
Aqualete Industries, LLC
Ocean, New Jersey
Phone: 1.732.695.6336
http://aqualeteindustries.com

Dry Flocculent Mixing System
Innovative Equipment Solutions
Hot Springs, Arkansas
Phone: 1.501.525.8484
http://www.neptunewash.com

OPTIONS ARE NOT LIMITED TO WHAT IS SHOWN ON THIS SHEET

NO MATTER THE SYSTEM OR METHOD USED, THE CONTRACTOR MUST MEET THE TERMS OF THE TEMPORARY DISCHARGE PERMIT AND THE STORMWATER PERMIT FOR CONSTRUCTION ACTIVITIES.

Various systems, devices, and products are shown on this sheet to give the Contractor ideas of what may be used for water treatment. Other systems, devices, and products are available and can be used with approval from the Engineer.

The Contractor may elect to block a portion of storm sewer near the outfall with sand bags and pump the water out to be treated with a flocculent or allow the water to set in a lined dumpster until sediment to falls out of suspension before discharging the water. Drop inlet protection devices could also be used as part of a treatment train. The Contractor may pump dirty water into a hydroseeder and mix it with a flocculent, and spray the mixture back onto a sediment pond.

PURPOSE

The purpose of a dewatering and sediment collection system is to collect turbid storm water on the project, treat it with flocculents as needed, and capture the sediment that falls out of suspension before the water is discharged into "Waters of the US" or "Waters of the State". Refer to the Environmental Commitments for the specific requirements for each body of water on this project.

The Contractor will need to create a Pollution Prevention Plan (PPP) for dewatering and sediment collection if the Contractor choses to discharge the water into "Waters of the US" or "Waters of the State" instead of disposing of the water off-site, using it for irrigation, or using it for hydroseeding. The Contractor will also need to obtain a Temporary Discharge Permit from the South Dakota Department of Agriculture & Natural Resources (DANR) on all projects outside of Indian Reservation boundaries.



Suggestions for dewatering and sediment collection may be shown on the plan sheets. It is the Contractor's responsibility to dewater and collect sediment. The Contractor will have to intercept and treat the stormwater before storm sewer outfalls into "Waters of the US" or "Waters of the State". The Contractor may need more than one dewatering and sediment collection system to capture and treat stormwater at multiple outfalls and/or locations simultaneously during each phase of the project.

PAYMENT

No additional payment will be made for Dewatering and Sediment Collecting. Dewatering and Sediment Collecting will be incidental to other items on the project.

THE CASCADE SYSTEM

The cascade system is shown below and to the right for conceptual purposes only; however, the cascade system will at a minimum incorporate the use of 2 flocculent housing units and 2 water and sediment storage units. Design and construction of the water and sediment storage units are project site specific and will be the Contractor's responsibility. A water and sediment storage unit may consist of a storage bin lined with plastic, the bed of a dump truck lined with plastic, a sediment basin, or other Engineer approved unit. The treatment flocculent bag may be from the list or an approved equal.

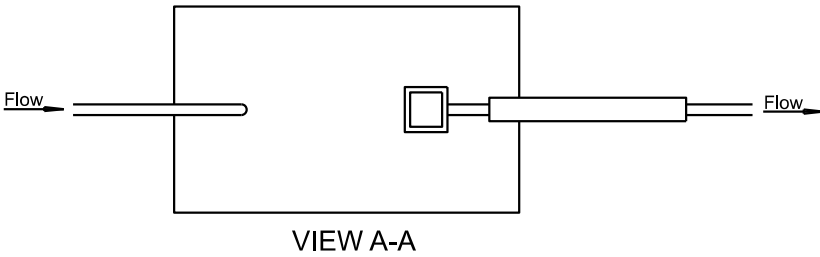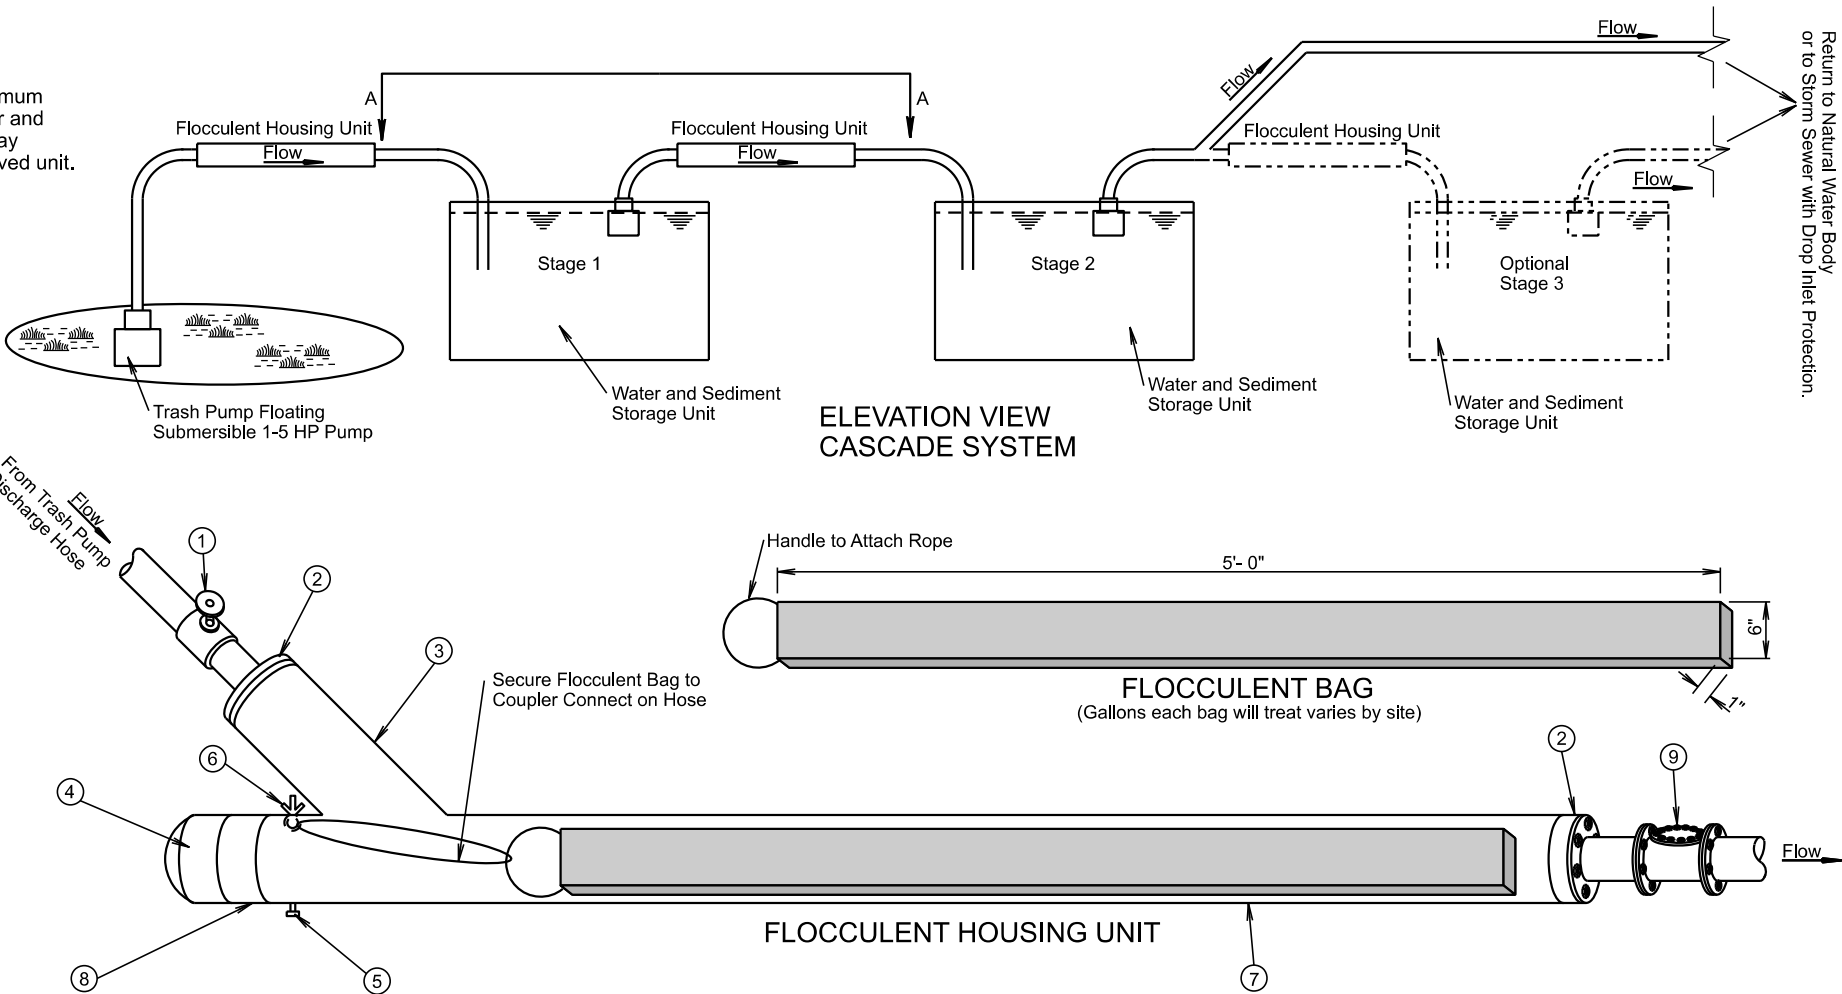

FLOCCULENT HOUSING UNIT (estimated quantities for information only)			
NO.	DESCRIPTION	QUANTITY	UNIT
1	4" or 6" Dia. Sch. 40 Gate Valve	1	Each
2	4" X 6" or 6" X 8" Sch. 40 PVC Bushing	2	Each
3	6" or 8" Dia. Sch. 40 PVC "Y"	1	Each
4	6" or 8" Dia. Sch. 40 PVC Female Threaded Cap	1	Each
5	1" Dia. Sch. 80 PVC Drain Valve	1	Each
6	1/2" Eye Bolt with Wing Nut and Rubber Gromets	1	Each
7	6" or 8" Dia. Sch. 40 PVC Pipe	10	Ft.
8	6" or 8" Dia. Sch. 40 PVC Male Adapter	1	Each
9	4" or 6" Dia. Sch. 40 PVC Swing Check Valve	1	Each



FLOW RATE ESTIMATE	
Pump Type	Flow Rate (gpm)
2"	50-250
3" Gas	250-350
4" Diesel	500-750
6" Diesel	750-1000

SDDOT CONSTRUCTION ENTRANCE




Plotting Date: 06/22/2026

PROJECT	SECTION	SHEET
NH-B 0212(194)266	D14	D19

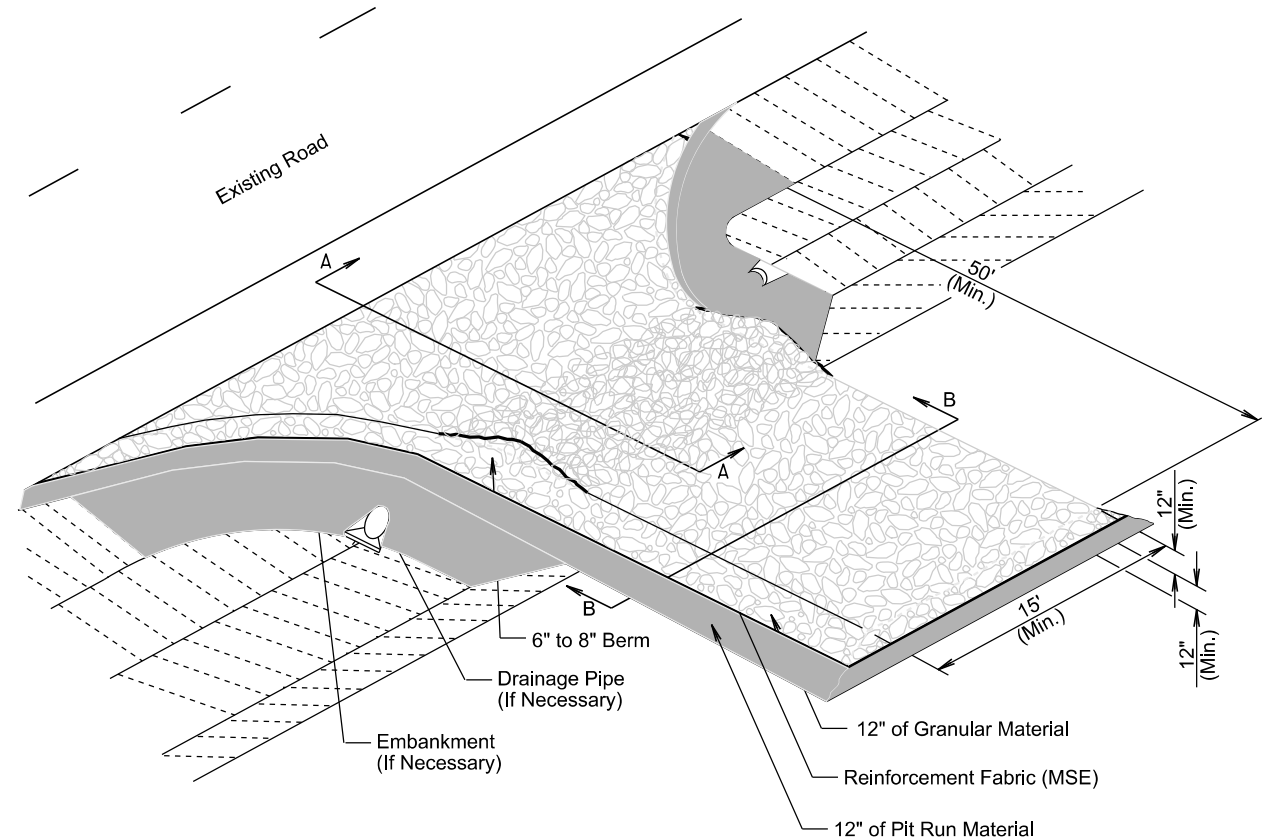

SECTION A-A



SECTION B-B



GENERAL NOTES:

If the grade of the entrance slopes down to the roadway, a berm of extra rock will be used to prevent sediment or mud from being deposited on the roadway. See SECTION A-A.


If a drainage pipe is necessary the size and type will be determined by the Contractor to meet field conditions. All cost will be incidental to the various contract items.

If embankment is necessary it will be pit run material.

TRANSVERSE TO ROADWAY

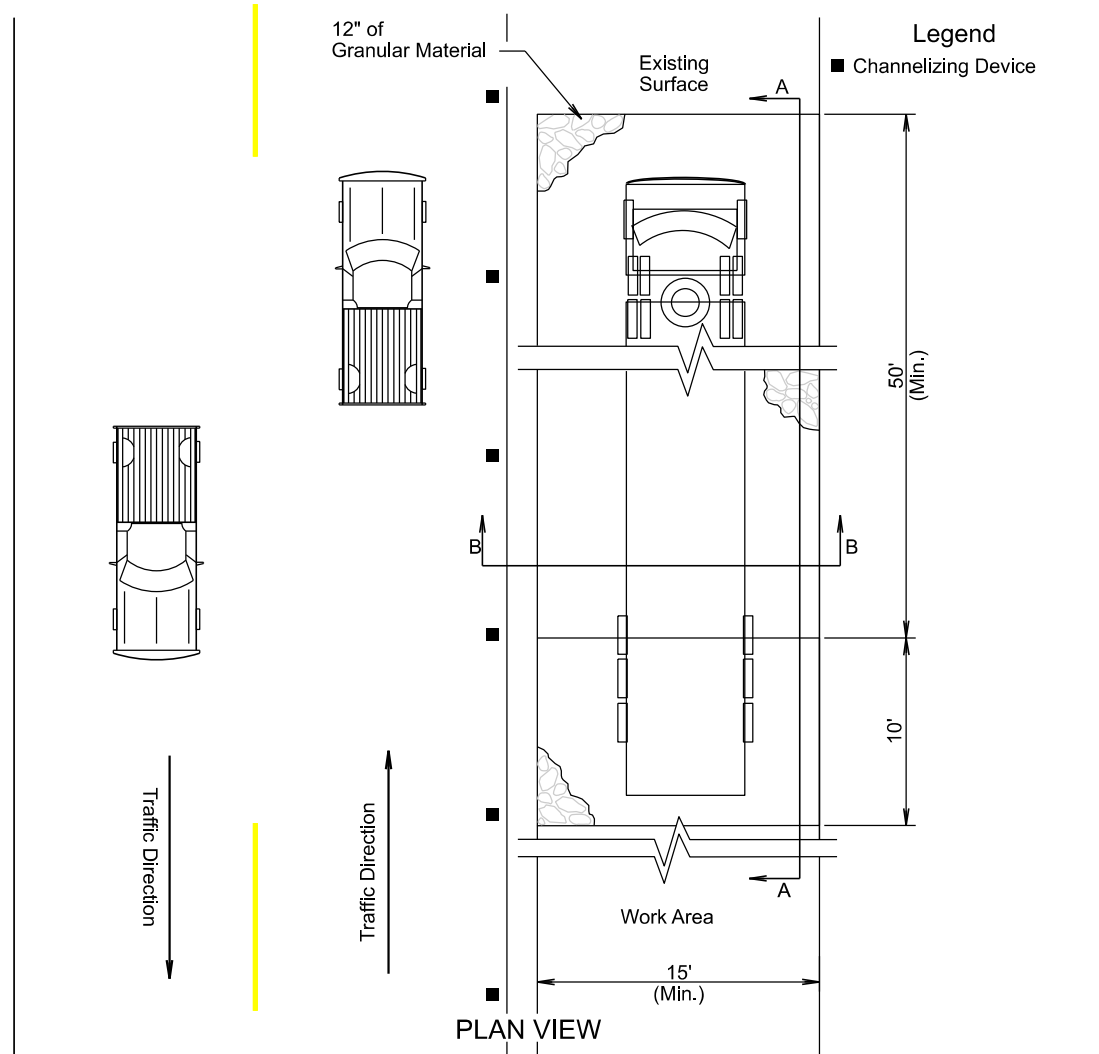


SECTION A-A



SECTION B-B

PARALLEL TO ROADWAY

MANUAL LOW FLOW SILT FENCE INSTALLATION

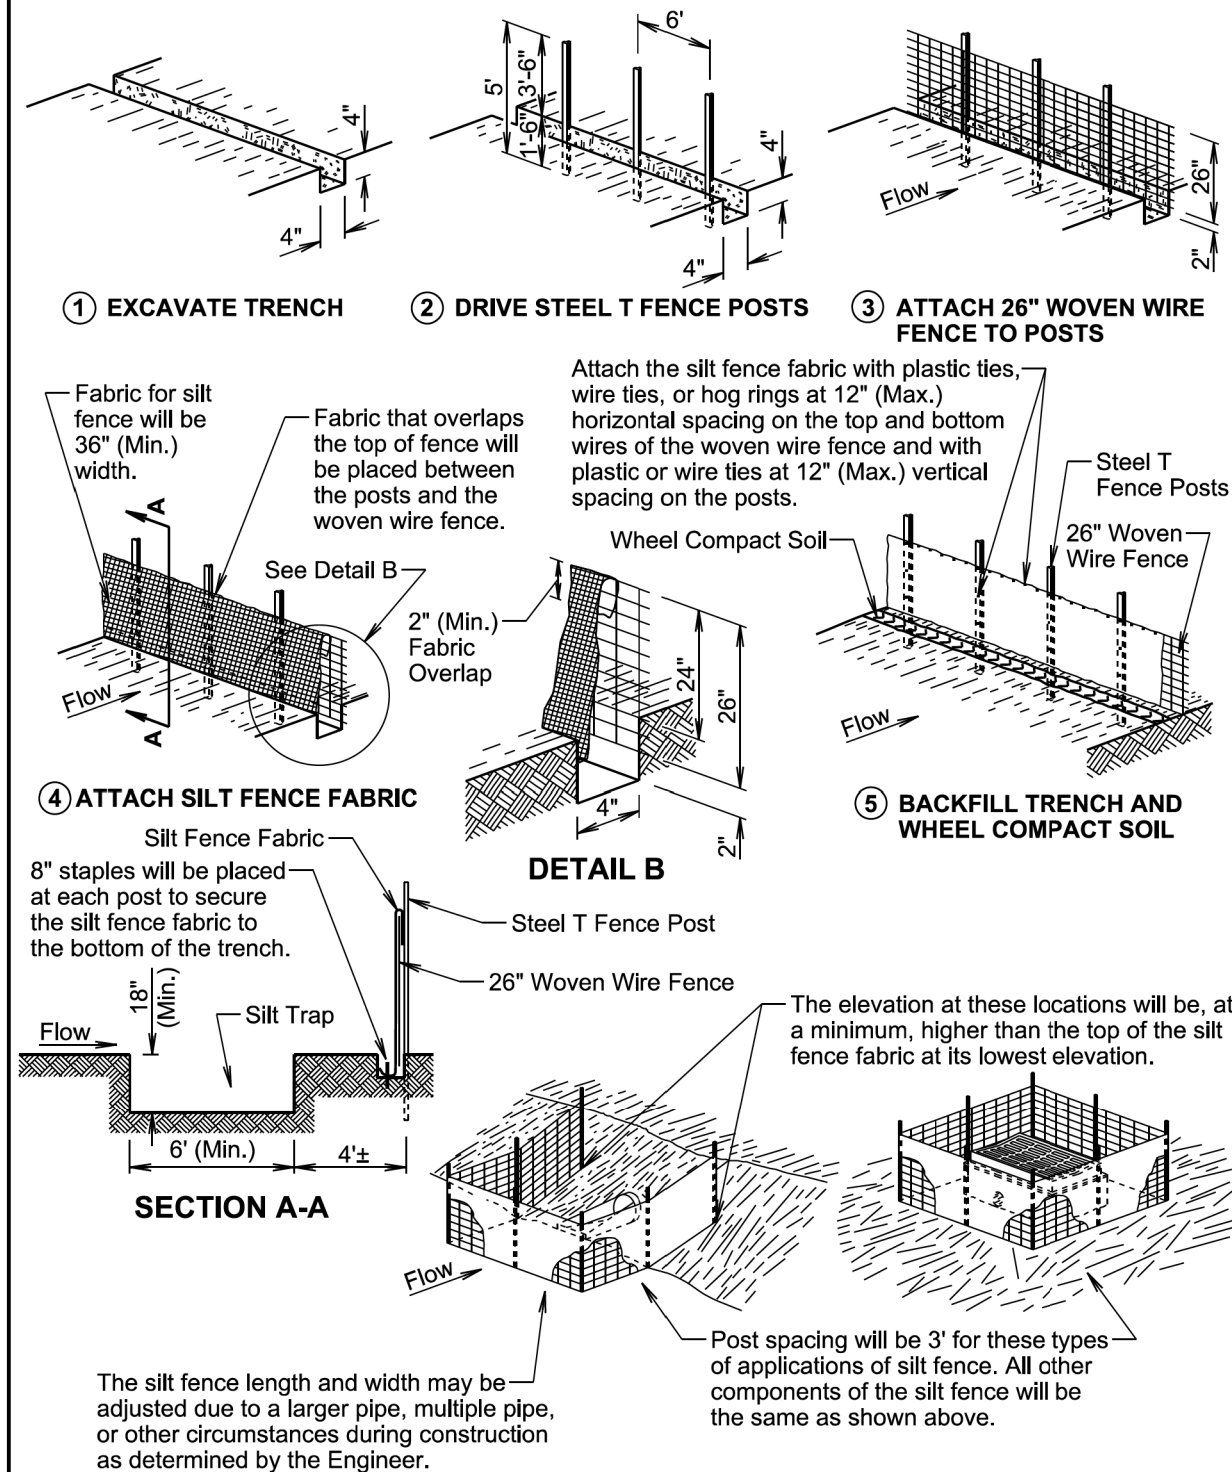

February 14, 2020

Published Date: 2027


SD
DOT

LOW FLOW SILT FENCE
AND SILT TRAP

PLATE NUMBER
734.04

Sheet 1 of 2

MACHINE SLICED LOW FLOW SILT FENCE INSTALLATION

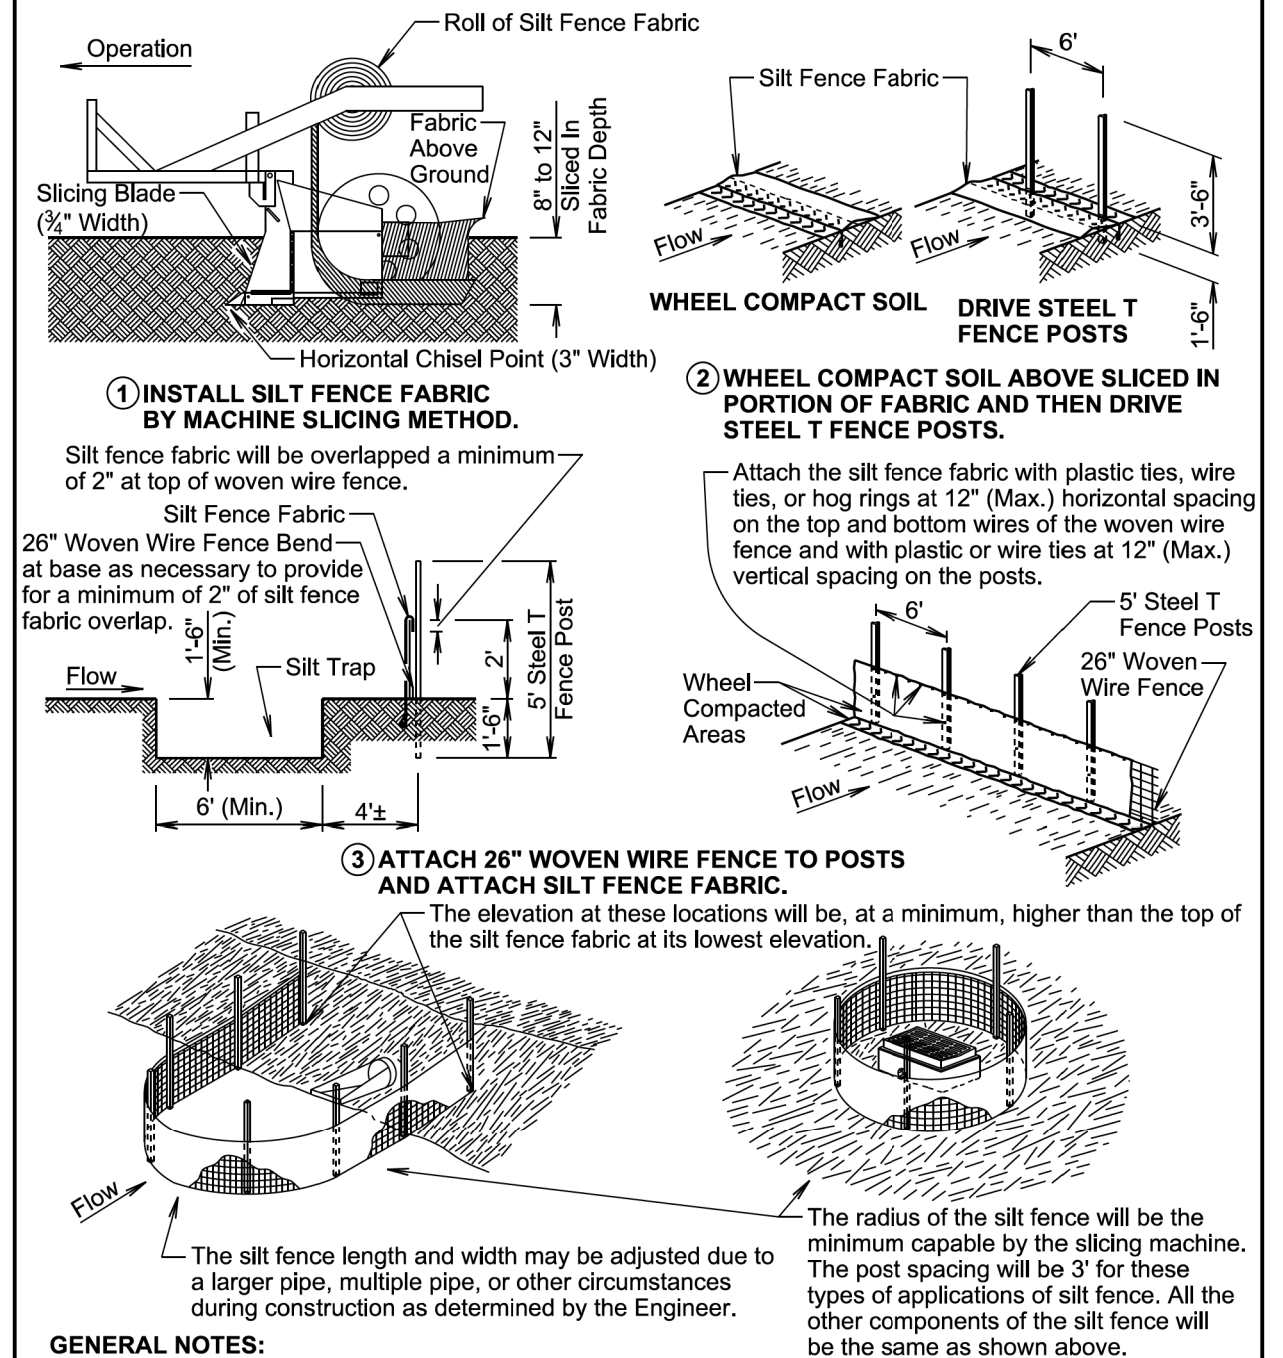

February 14, 2020

Published Date: 2027


SD
DOT

LOW FLOW SILT FENCE
AND SILT TRAP

PLATE NUMBER
734.04

Sheet 2 of 2

MANUAL HIGH FLOW SILT FENCE INSTALLATION

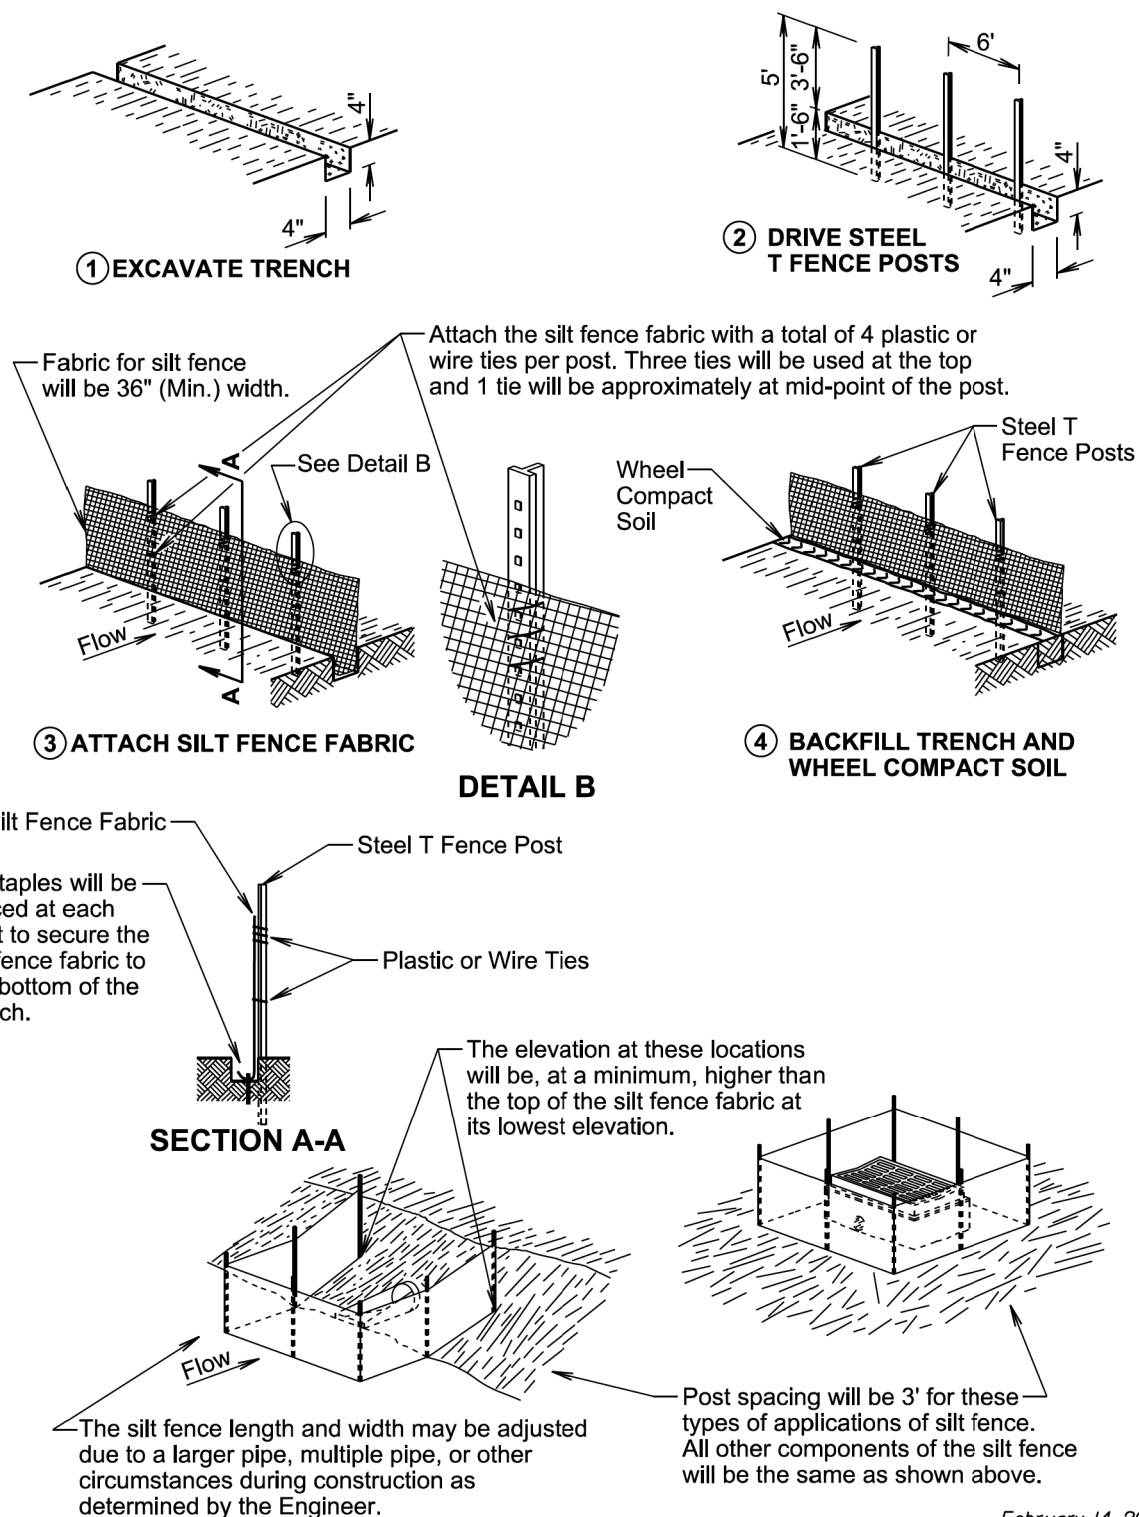

February 14, 2020

Published Date: 2027


SD
DOT

HIGH FLOW SILT FENCE

PLATE NUMBER
734.05

Sheet 1 of 2

MACHINE SLICED HIGH FLOW SILT FENCE INSTALLATION

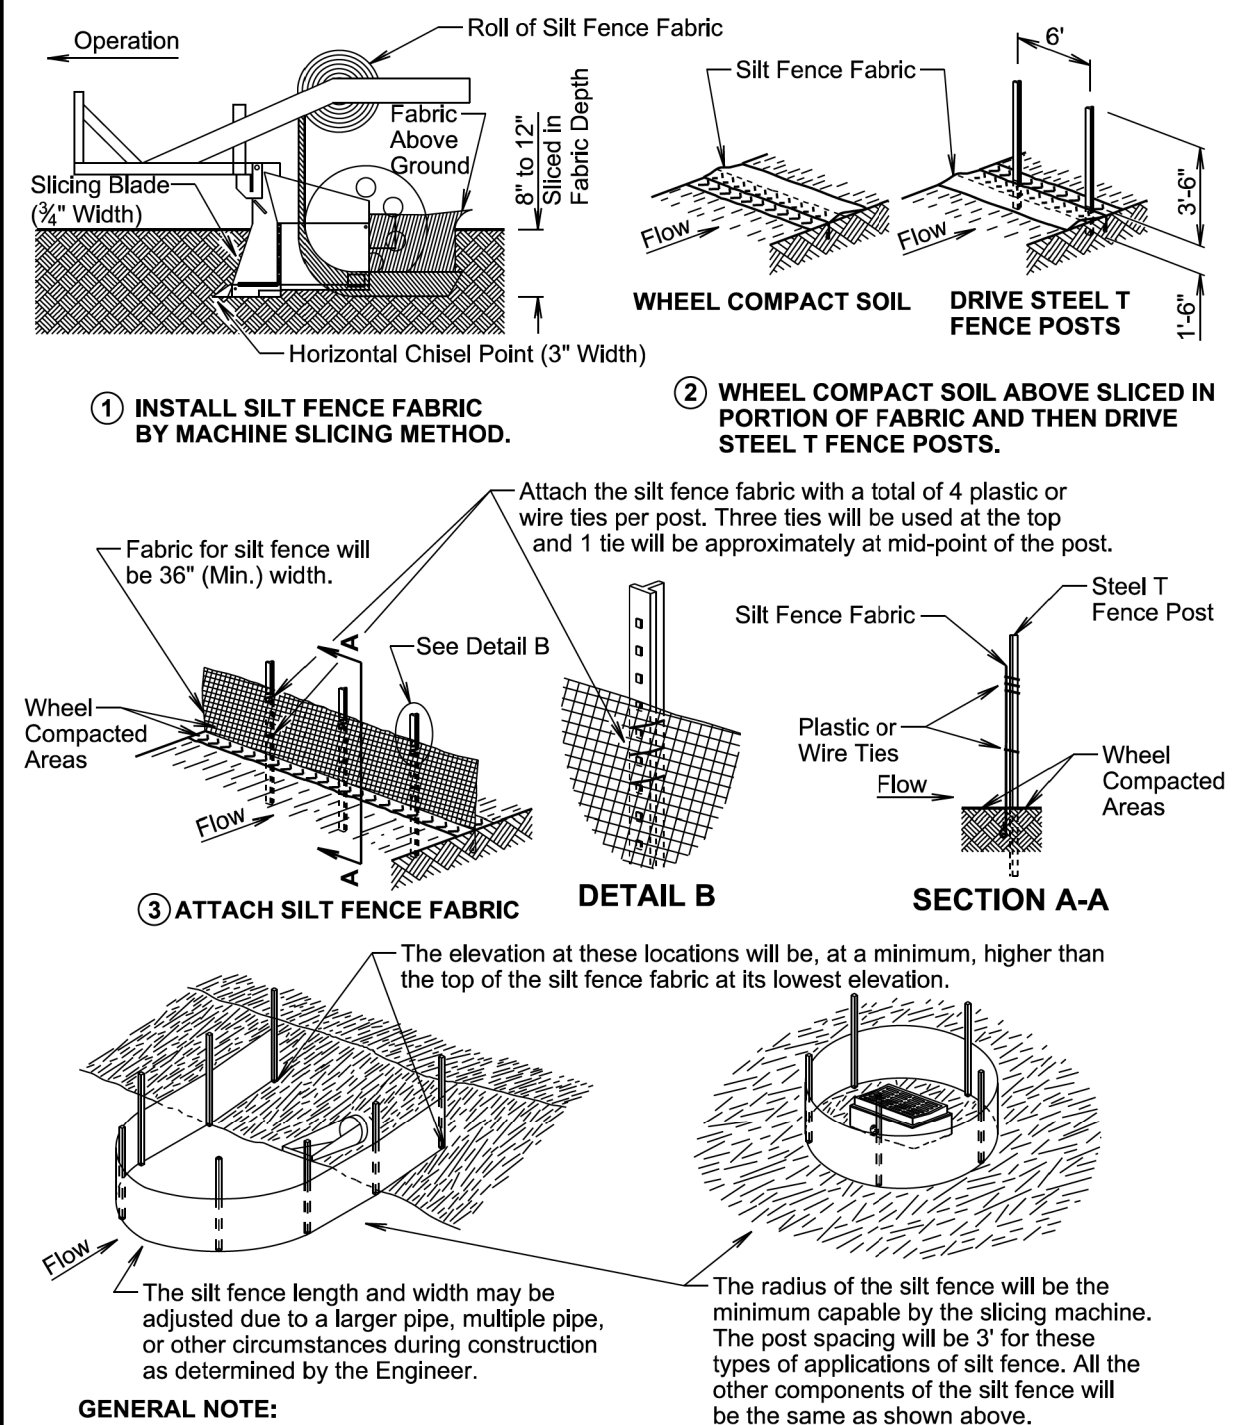

February 14, 2020


Published Date: 2027

SD
DOT

HIGH FLOW SILT FENCE


PLATE NUMBER
734.05

Sheet 2 of 2

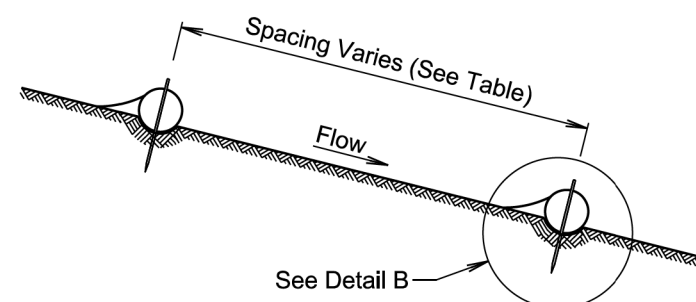


ELEVATION VIEW (Cut or Fill Slope Installation)


CUT OR FILL SLOPE INSTALLATION	
Slope	Spacing (Ft.)
1:1	10
2:1	20
3:1	30
4:1	40

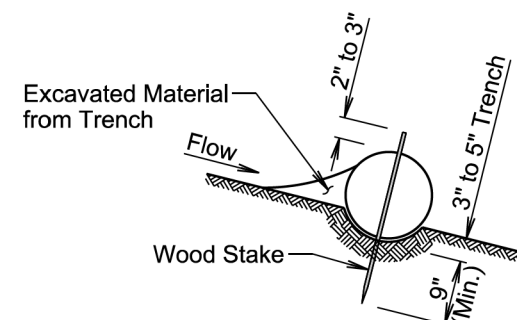


DETAIL B
(Typical of All Installations)

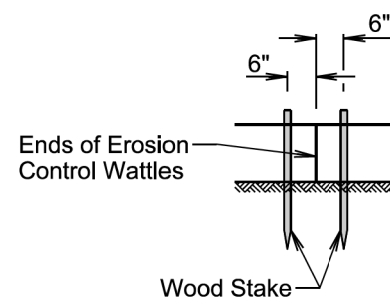


DETAIL C
(See General Notes)

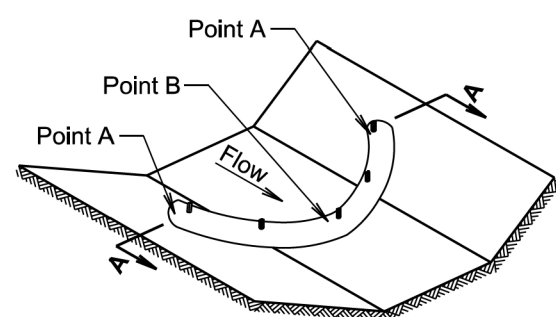

ISOMETRIC VIEW (Ditch Installation)

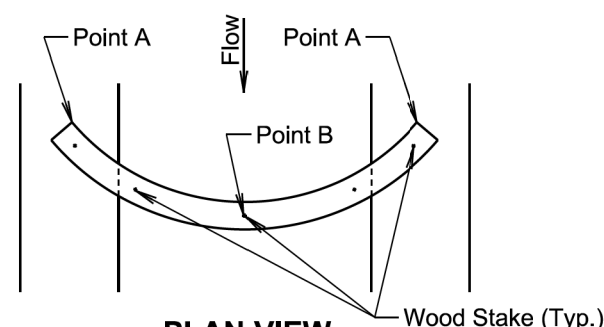

PLAN VIEW (Ditch Installation)



SECTION A-A

DITCH INSTALLATION	
Grade	Spacing (Ft.)
2%	150
3%	100
4%	75
5%	50

February 14, 2020

Published Date: 2027

SDDOT

EROSION CONTROL WATTLE

PLATE NUMBER
734.06

Sheet 1 of 2

February 14, 2020


Published Date: 2027

SD
D
D
O
T

EROSION CONTROL WATTLE

PLATE NUMBER
734.06

Sheet 2 of 2

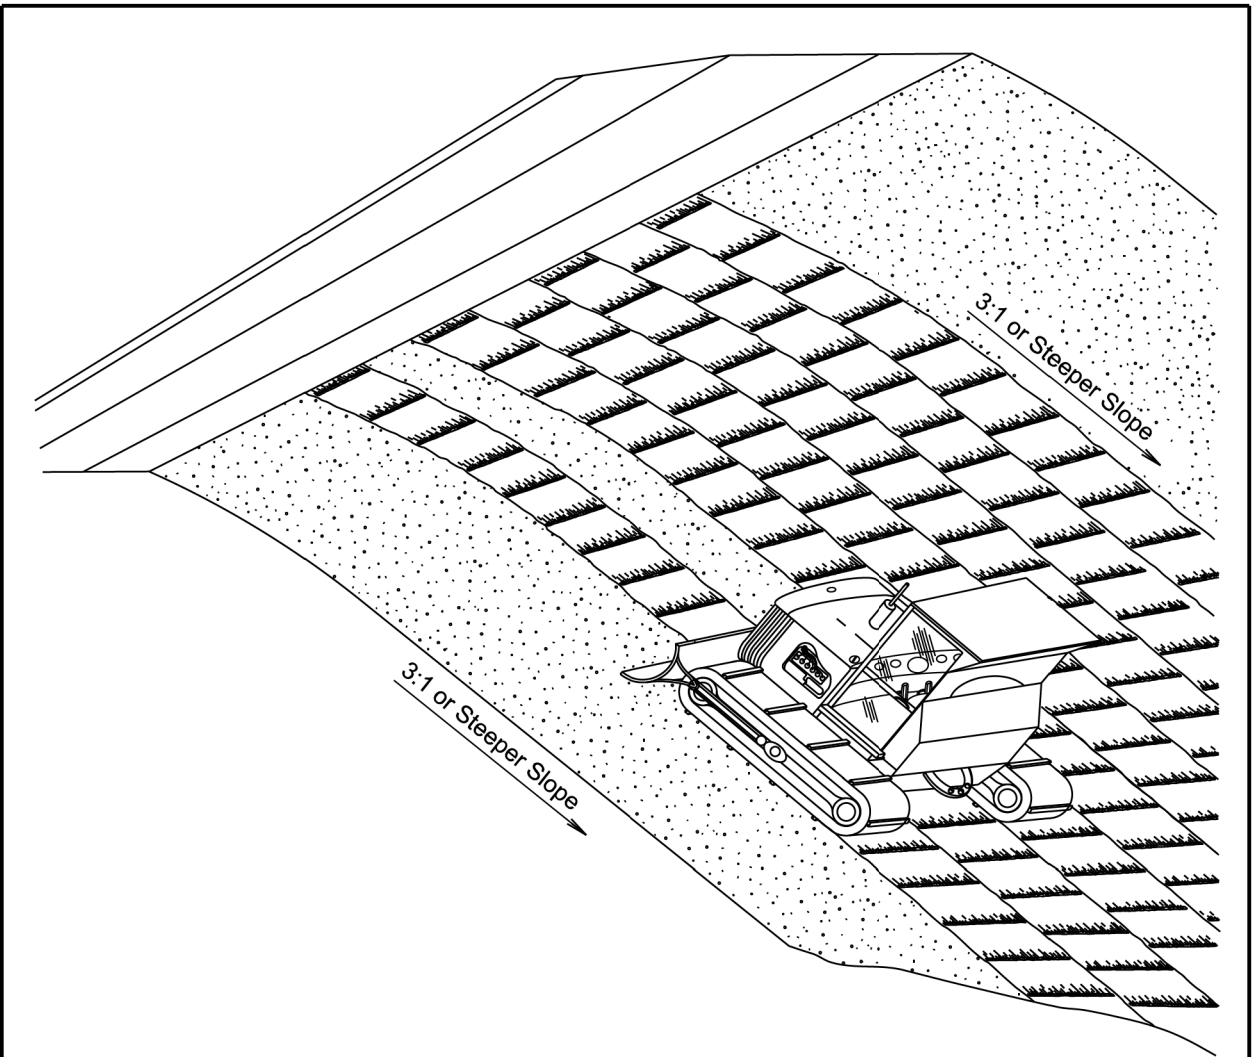

GENERAL NOTES:

Where practical, surface roughening will be done on slopes 3:1 and steeper and on slopes deemed necessary by the Engineer.

The equipment used for surface roughening will be equipped with tracks that are capable of creating ridges in the soil that are perpendicular to the slope. The final condition of the surface roughening will be approved by the Engineer.

Measurement for surface roughening will be to the nearest tenth of an acre.

All costs associated with surface roughening including labor, equipment, and materials will be incidental to the contract unit price per acre for "Surface Roughening".

February 14, 2020

<i>Published Date: 2027</i>	SD DOT	SURFACE ROUGHENING	PLATE NUMBER 734.25
			<i>Sheet 1 of 1</i>
