


Section C: Traffic Control Plans

STATE OF SOUTH DAKOTA	PROJECT	SHEET	TOTAL SHEETS
	EM 0073(73)62	C1	C9

Plotting Date: 05/15/2024

INDEX OF SHEETS

- C1 General Layout with Index
- C2 - C3 Estimate of Quantities, General Notes, and Tables
- C4 - C5 Sign Tab and Layout Details
- C6 - C9 Standard Plates

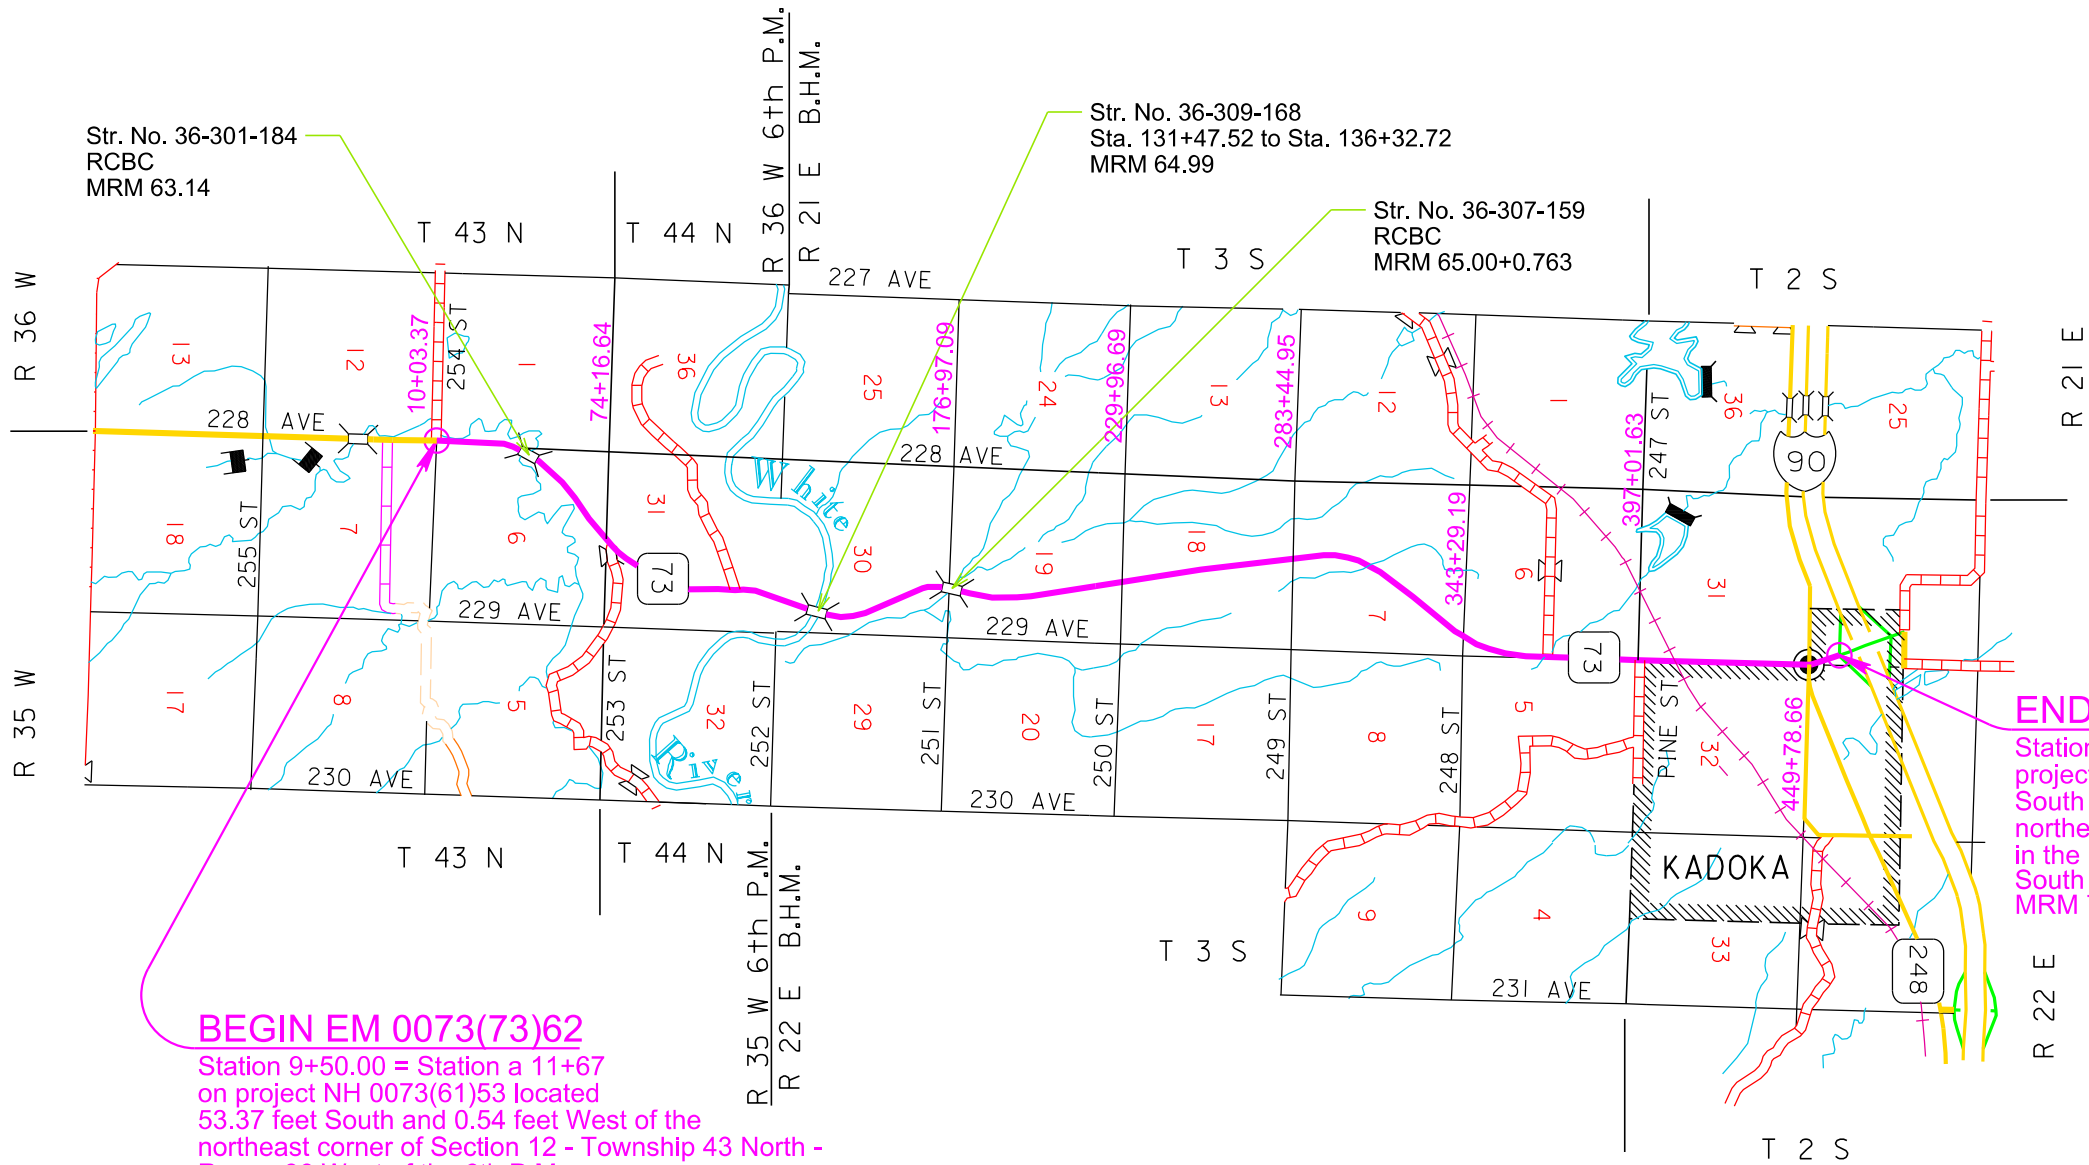

BEGIN EM 0073(73)62
Station 9+50.00 = Station a 11+67
on project NH 0073(61)53 located
53.37 feet South and 0.54 feet West of the
northeast corner of Section 12 - Township 43 North -
Range 36 West of the 6th P.M.
MRM 62.00+0.399

END EM 0073(73)62
Station 462+77.23 = Station g 22+56.56 on
project NH 0073(61)53 located 7.95 feet
South and 253.21 feet East of the
northeast corner of Lot B of Merchen Tract 1
in the SE1/4 SE1/4 of Section 30 - Township 2
South - Range 22 East of the B.H.M.
MRM 71.09+0.111

ESTIMATE OF QUANTITIES

BID ITEM NUMBER	ITEM	QUANTITY	UNIT
633E1200	High Build Waterborne Pavement Marking Paint, White	386	Gal
633E1205	High Build Waterborne Pavement Marking Paint, Yellow	246	Gal
634E0010	Flagging	1,000.0	Hour
634E0020	Pilot Car	400.0	Hour
634E0110	Traffic Control Signs	447.8	SqFt
634E0120	Traffic Control, Miscellaneous	Lump Sum	LS
634E0630	Temporary Pavement Marking	34.0	Mile

SEQUENCE OF OPERATIONS

The Contractor will submit a sequence of operations for approval two weeks prior to the preconstruction meeting. If changes to the sequence of operations are proposed during the project, these must be submitted for review a minimum of one week prior to potential implementation. Approval for changes to the sequence of operations will only be allowed when the proposed changes meet with the Department’s intent for traffic control and sequencing of the work.

Rumble stripes and the flush seal will be completed prior to permanent pavement marking.

GENERAL TRAFFIC CONTROL

Existing guide, route, informational logo, regulatory, and warning signs will be temporarily reset and maintained during construction. Removing, relocating, covering, salvaging, and resetting of existing traffic control devices, including delineation, will be the responsibility of the Contractor. Cost for this work will be incidental to the contract unit prices for the various items unless otherwise specified in the plans. Any delineators and signs damaged or lost will be replaced by the Contractor at no cost to the State.

All temporary traffic control sign locations will be set in the field by the Contractor and verified by the Engineer prior to installation.

All construction operations will be conducted in the general direction of traffic movement.

If there is a discrepancy between the traffic control plans, standard plates, and the MUTCD, whichever is more stringent will be used, as determined by the Engineer.

Unless otherwise stated in these plans, work will not be allowed during hours of darkness.

Fixed location signing placed more than 4 calendar days prior to the start of construction will be covered or laid down until the time of construction. The covers must be approved by the Engineer prior to installation. The cost of materials, labor, and equipment necessary to complete this work will be incidental to other contract items. No separate payment will be made.

All fixed location signs, sign posts, and breakaway bases will be removed within 7 calendar days following pavement marking.

All haul trucks will be equipped with an additional flashing amber light that is visible from the backside of the haul truck. The costs for the flashing amber lights will be incidental to the various related contract items.

Traffic will be maintained on the driving lanes. Use of the shoulder as a driving lane will not be permitted. Any damage to the shoulder due to rerouted traffic or Contractor’s equipment will be repaired at no expense to the Department.

The Contractor will furnish, install, maintain, and remove TRUCK CROSSING (W8-6) signs daily. The TRUCK CROSSING signs will be displayed always when haul vehicles are hauling material. When hauling conditions no longer exist, the signs will be covered or removed from view. The exact number and location will be determined during construction. Payment for additional signs will be based on the contract unit price per square foot for “Traffic Control Signs”.

A mobile work operation will be allowed provided the rumble strip or rumble stripe grooving, flush sealing, and pavement marking can be completed satisfactorily by a continuously moving work operation. A mobile work operation will require approval by the Engineer.


Contractor will accommodate all over width traffic during the duration of the project.

BUMP signs will be used in conjunction with the transitions at the end of the day.

FLAGGING

Operations will be conducted so that the traveling public will not have to wait longer than 15 minutes at the flagger station.

Additional flagger warning signs and flagger hours have been included in the Estimate of Quantities for use on intersecting roads. These flaggers will be used as directed by the Engineer and will be used primarily during daytime hours. Also included in the Estimate of Quantities are WAIT FOLLOW PILOT CAR signs for use on low volume intersecting roads as determined by the Engineer. WAIT FOLLOW PILOT CAR signs will not block the view of the stop sign.

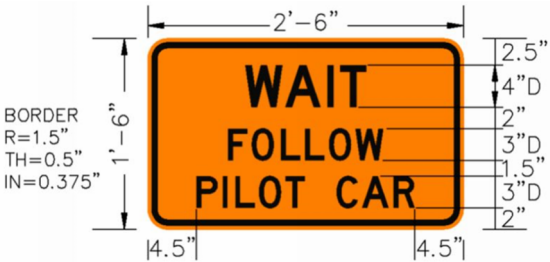

It is required that the flaggers and pilot car operators be able to communicate with one another. If an emergency vehicle needs to pass through the project, the Contractor will be required to expedite traffic movement. All costs associated with this will be incidental to the contract unit price per hour for “Flagging”.

INCIDENTS

An incident is an emergency road user occurrence, a natural disaster, or other unplanned event that affects or impedes the normal flow of traffic such as a crash, hazardous materials spill, or other event.

The Contractor will set up a meeting prior to start of work to plan and coordinate responses to an incident. The Contractor will invite the Department of Transportation, the South Dakota Highway Patrol, the Jackson County Sheriff and local emergency response entities to the meeting.

The Contractor will assist to maintain traffic as required by these plan notes and as agreed to at that meeting.

Emergency vehicle access through the project will be considered and discussed at the meeting.

The Contractor should be prepared to relocate advance warning signs if determined to be necessary for a major traffic incident lasting more than two hours. Fixed location ground mounted signs may be covered and additional portable signs provided.

Cost for the relocation of an advance warning sign due to an incident will be 50% of the designated sign rate. Flaggers will be paid for at the contract unit price per hour for “Flagging”.

PRESS RELEASE ANNOUNCEMENTS

The SDDOT will prepare a press release to be released 5 days prior to any phase change or any other major change that affects traffic flow. The SDDOT will be responsible to keep law enforcement, emergency services, and the traveling public notified of changes in project access. The Contractor will provide the Engineer with pertinent information 7 days prior to any phase change or any other major change that affects traffic flow.

TEMPORARY PAVEMENT MARKING

The total length of no passing zone on this project is estimated to be 4.13 miles.

It is estimated that 17 DO NOT PASS (R4-1) and 18 PASS WITH CARE (R4-2) signs will be required to mark the no passing zones, should the Contractor elect to use these signs.

Temporary flexible vertical markers (tabs) will be used to mark dashed centerline, No Passing Zones, and applicable lane lines. Paint will not be allowed for temporary pavement marking on the asphalt concrete wear course or after application of the flush seal.

Covers on the tabs will be sufficiently secured to prevent traffic from dislodging the cover and when removed, the covers will be properly disposed of. The Contractor will remove and properly dispose of the tabs after permanent pavement marking is applied. Method of removal will be nondestructive to the road surface and will be accomplished within one week of completion of the permanent pavement marking.

Any temporary flexible vertical markers (tabs) with covers removed before the flush seal will be replaced prior to application of the flush seal. Full reflectivity of all temporary flexible vertical markers (tabs) is required at all times. The Contractor will be required to replace any missing or non-reflective tabs after each installation as detailed below at no additional cost to the State.

Quantities of Temporary Pavement Markings consist of:

- One pass on top of the asphalt concrete first lift
- One pass on top of the asphalt concrete final lift
- One pass prior to the flush seal, length as determined by the Engineer
- One pass on top of the flush seal

STATE OF SOUTH DAKOTA	PROJECT	SHEET NO.	TOTAL SHEETS
	EM 0073(73)62	C3	C9

TEMPORARY PAVEMENT MARKING (CONTINUED)

If the flush seal is eliminated, the application of the temporary pavement marking on top of the flush seal will be eliminated. No adjustment in the contract unit price for “Temporary Pavement Marking” will be made because of a variation in quantities.

In the absence of a signed lane closure or pilot car operation, FLAGGER (W20-7) symbol signs and flaggers, or a shadow vehicle with rotating yellow lights or strobe lights will be positioned on the shoulder in advance of workers for both directions of traffic during the installation and removal of the temporary flexible vertical markers (tabs). The traffic control device used will be moved intermittently to provide proper warning of the work operation. A ROAD WORK AHEAD (W20-1) sign, a WORKER (W21-1) symbol sign or a BE PREPARED TO STOP (W3-4) sign will be mounted on the rear of the shadow vehicle. The method of traffic control used by the Contractor for this work must be approved by the Engineer.

Prior to nightfall, tabs will be required to mark centerline on segments of roadway where existing centerline markings have been removed and new markings have not been installed.

PERMANENT PAVEMENT MARKING

The Contractor will be required to repaint all existing pavement markings including centerline, edge line, and lane lines. This list is approximate. The Contractor will be required to document and be able to relocate for replacement of the existing markings before they are obliterated. The cost to duplicate the existing marking locations will be incidental to the contract unit prices for the various contract items.

PAVEMENT MARKING PAINT

All materials will be applied as per the manufacturer’s recommendations.

The Contractor will advise the Engineer a minimum of 3 weeks prior to the application of the permanent pavement marking to allow the State to check and mark the location of no passing zones.

The application of permanent pavement marking will begin no sooner than 7 calendar days following completion of the flush seal. Application of permanent pavement marking will be completed within 14 calendar days following completion of the final surfacing.

HIGH BUILD WATERBORNE PAVEMENT MARKING PAINT

All materials will be applied as per manufacturer’s recommendations. High build waterborne pavement marking paint will conform to the supplemental specifications for Section 980.1 B.

Reflective media will consist of glass beads. Reflective media will require a Certificate of Compliance for Certification for each source and lot. Acceptance sampling will not be required.

RATES OF MATERIALS FOR HIGH BUILD WATERBORNE PAVEMENT MARKING PAINT

Solid 4” line = 22.5 Gals/Mile
Dashed 4” line = 6.2 Gals/Mile
Glass Beads = 8 Lbs/Gal.

All cost for materials, labor and equipment necessary to furnish and install the pavement markings will be incidental to the contract unit price for the respective High Build Waterborne Pavement Marking Paint items.

RETROREFLECTIVITY FOR PAVEMENT MARKING PAINT


The Department may take retroreflectivity readings on the pavement marking lines after 2 days and within 30 days of the line application using either a portable or mobile retroreflectometer that conforms to 30-meter geometry. If the Department chooses to take retroreflectivity readings, three retroreflectivity readings will be taken on each line at each test location. The three readings will be averaged and become the reading for that test location.

If the Department chooses to take retroreflectivity readings, three readings will be taken on the edge lines and lane lines in the direction of application. For combination solid yellow and skip yellow lines for turn lanes and for centerline markings on two-way roadways, three readings will be taken in one direction, the reflectometer will be turned 180 degrees and three more readings will be taken. The six readings for the centerline markings will be averaged and become the test reading for that test location.

If the Department chooses to take readings, the minimum retroreflectivity values will be 275 mc/m²/lux for white and 170 mc/m²/lux for yellow.

ITEMIZED LIST FOR TRAFFIC CONTROL SIGNS

SIGN CODE	SIGN DESCRIPTION	CONVENTIONAL ROAD			
		NUMBER	SIGN SIZE	SQFT PER SIGN	SQFT
W8-1	BUMP	2	48" x 48"	16.0	32.0
W8-6	TRUCK CROSSING	2	48" x 48"	16.0	32.0
W8-11	UNEVEN LANES	2	48" x 48"	16.0	32.0
W13-1P	ADVISORY SPEED (plaque)	2	30" x 30"	6.3	12.6
W20-1	ROAD WORK AHEAD	8	48" x 48"	16.0	128.0
W20-4	ONE LANE ROAD AHEAD	2	48" x 48"	16.0	32.0
W20-7	FLAGGER (symbol)	2	48" x 48"	16.0	32.0
W21-2	FRESH OIL	2	48" x 48"	16.0	32.0
W21-3	ROAD MACHINERY AHEAD	2	48" x 48"	16.0	32.0
W21-5	SHOULDER WORK	2	48" x 48"	16.0	32.0
SPECIAL	WAIT FOLLOW PILOT CAR	4	30" x 18"	3.8	15.2
G20-1	ROAD WORK NEXT __ MILES	2	36" x 18"	4.5	9.0
G20-2	END ROAD WORK	6	36" x 18"	4.5	27.0
		CONVENTIONAL ROAD TRAFFIC CONTROL SIGNS SQFT			
		447.8			

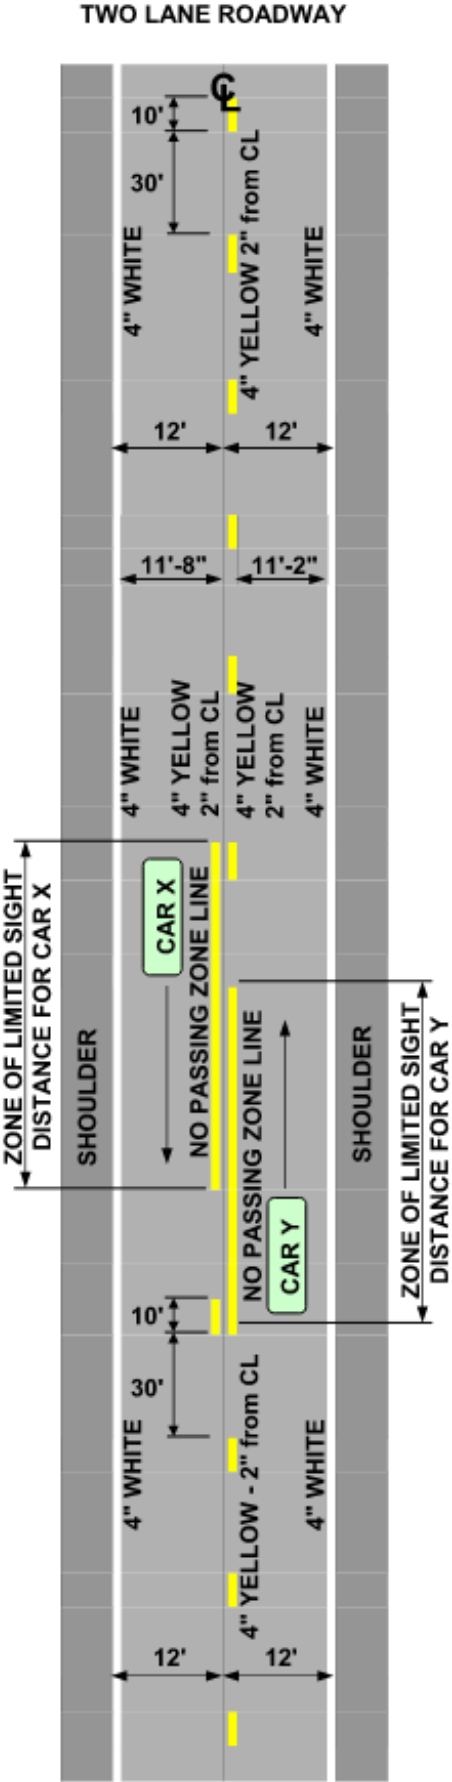

PAVEMENT MARKING

Typical pavement marking as shown on this sheet will be applied throughout the entire length of two lane roadway.

Traffic Control will be incidental to the cost of application. The striper and advance or trailing warning vehicle will be equipped with flashing amber lights and advance warning arrow board.

Application rates will be as follows:

Two Lane Roadway (Rates for one line)
Dashed Yellow Centerline Rate = 6.2 Gals./Pass-Mile
Solid Yellow Centerline Rate = 22.5 Gals./Pass-Mile
Solid White Edgeline Rate = 22.5 Gals./Pass-Mile


4" Yellow Skip Centerline (when not adjacent to a 4" Yellow No Passing Zone) will be placed consistently to the south or east side of centerline.

ESTIMATED QUANTITIES (BASED ON ONE APPLICATION)	
PAINT	QUANTITY
WHITE	386 GALLONS
YELLOW	246 GALLONS

FIXED LOCATION SIGN LAYOUT

STATE OF SOUTH DAKOTA	PROJECT	SHEET	TOTAL SHEETS
	EM 0073(73)62	C5	C9

Plotting Date: 05/15/2024

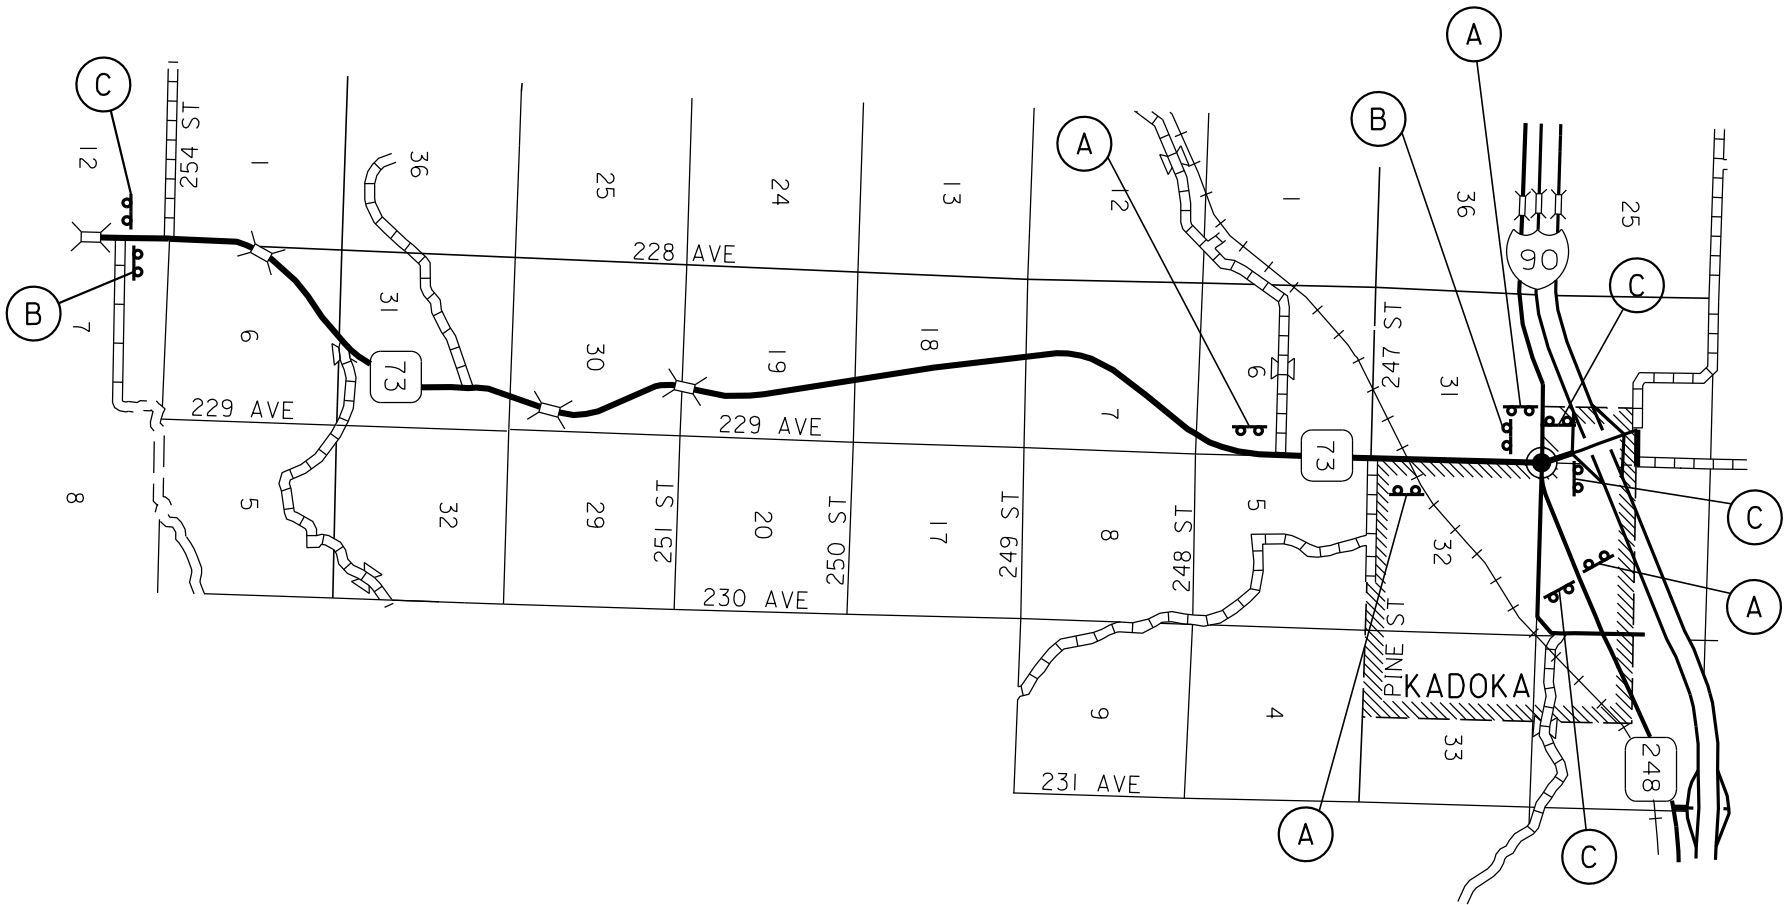

A = ROAD WORK AHEAD
W20-1
(48"X48")

B = ROAD WORK NEXT 12 MILES
G20-1
(48"X24")

C = END ROAD WORK
G20-2A
(48"X24")


The signs illustrated are not required if the work space is behind a barrier, more than 2 feet behind the curb, or 15 feet or more from the edge of any roadway.

The signs illustrated will be used where there are distracting situations; such as: vehicles parked on shoulder, vehicles accessing the work site via the highway, and equipment traveling on or crossing the roadway to perform work operations.

The ROAD WORK AHEAD sign may be replaced with other appropriate signs, such as the SHOULDER WORK sign. The SHOULDER WORK sign may be used for work adjacent to the shoulder.

* If the work space is on a divided highway, an advance warning sign should also be placed on the left side of the directional roadway.

For short term, short duration, or mobile operations, all signs and channelizing devices may be eliminated if a vehicle with an activated flashing or revolving yellow light is used.



Posted Speed Prior to Work (M.P.H.)	Spacing of Advance Warning Signs (Feet) (A)
0 - 30	200
35 - 40	350
45 - 50	500
55	750
60 - 80	1000



January 22, 2021

Published Date: 2024	S D D O T	WORK BEYOND THE SHOULDER	PLATE NUMBER 634.01
			Sheet 1 of 1

*In situations where multiple work locations in a limited distance make it practical to place stationary signs, the distance between the advance warning sign and the work should not exceed 5 miles.



The ROAD WORK NEXT xx MILES sign may be used instead of the ROAD WORK AHEAD sign if the work locations occur over a distance of more than 2 miles.

Arrow board is required for intermittently and continuously moving mobile operations when work exceeds 1 hour.

**If the work space is on a divided highway, an advance warning sign should also be placed on the left side of the directional roadway.

In situations where the distance between the advance warning signs and the work is 2 miles to 5 miles, a Supplemental Distance plaque should be used with the ROAD WORK AHEAD sign.

All costs associated with the traffic control for mobile operation including signs, arrow boards and equipment will be incidental to the contract lump sum price for "Traffic Control, Miscellaneous".

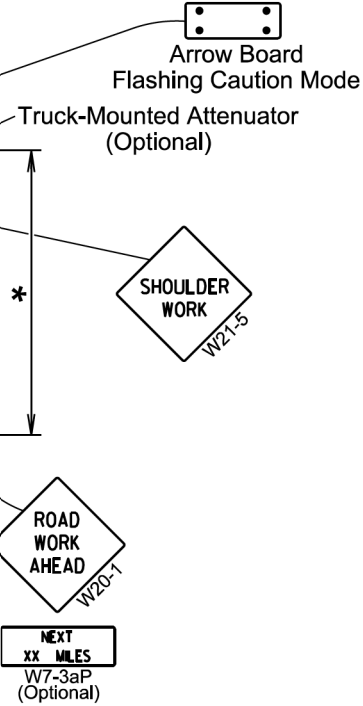

January 22, 2021

Published Date: 2024	S D D O T	MOBILE OPERATIONS ON SHOULDERS	PLATE NUMBER 634.04
			Sheet 1 of 1

Plotted From: - TRPR25289 1:200 Plot Scale -

STATE OF SOUTH DAKOTA	PROJECT	SHEET	TOTAL SHEETS
	EM 0073(73)62	C7	C9

Plotting Date: 04/04/2024

* Messages on signs will vary depending on the operation being conducted.

Vehicle-mounted signs will be mounted in a manner such that they are not obscured by equipment or supplies. Sign legends on vehicle-mounted signs will be covered or turned from view when work is not in progress.


Shadow and Work vehicles will display high-intensity rotating, flashing, oscillating, or strobe lights, flags, signs, or arrow boards.

Vehicle hazard warning signals will not be used instead of the vehicle's high-intensity rotating, flashing, oscillating, or strobe lights.

When an arrow board is used, it will be used in the caution mode. Marching Diamonds are acceptable.

Arrow boards will, as a minimum, be Type B, with a size of 60" x 30".


All costs associated with the traffic control for mobile operation including signs, arrow boards and equipment will be incidental to the contract lump sum price for "Traffic Control, Miscellaneous".

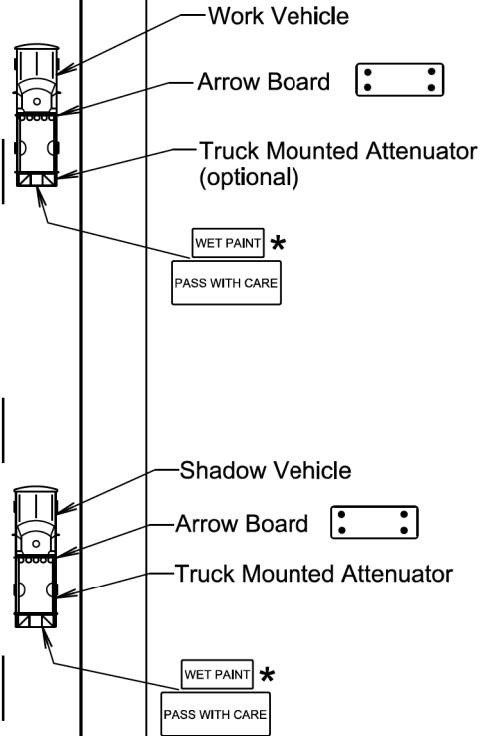

January 22, 2021

Published Date: 2024	S D D O T	MOBILE OPERATIONS ON 2-LANE ROAD	PLATE NUMBER 634.06
			Sheet 1 of 1

Install additional UNEVEN LANES signs at 2 mile intervals throughout the entire length of the uneven area and at affected major intersections, edge of towns, and other sites deemed necessary.


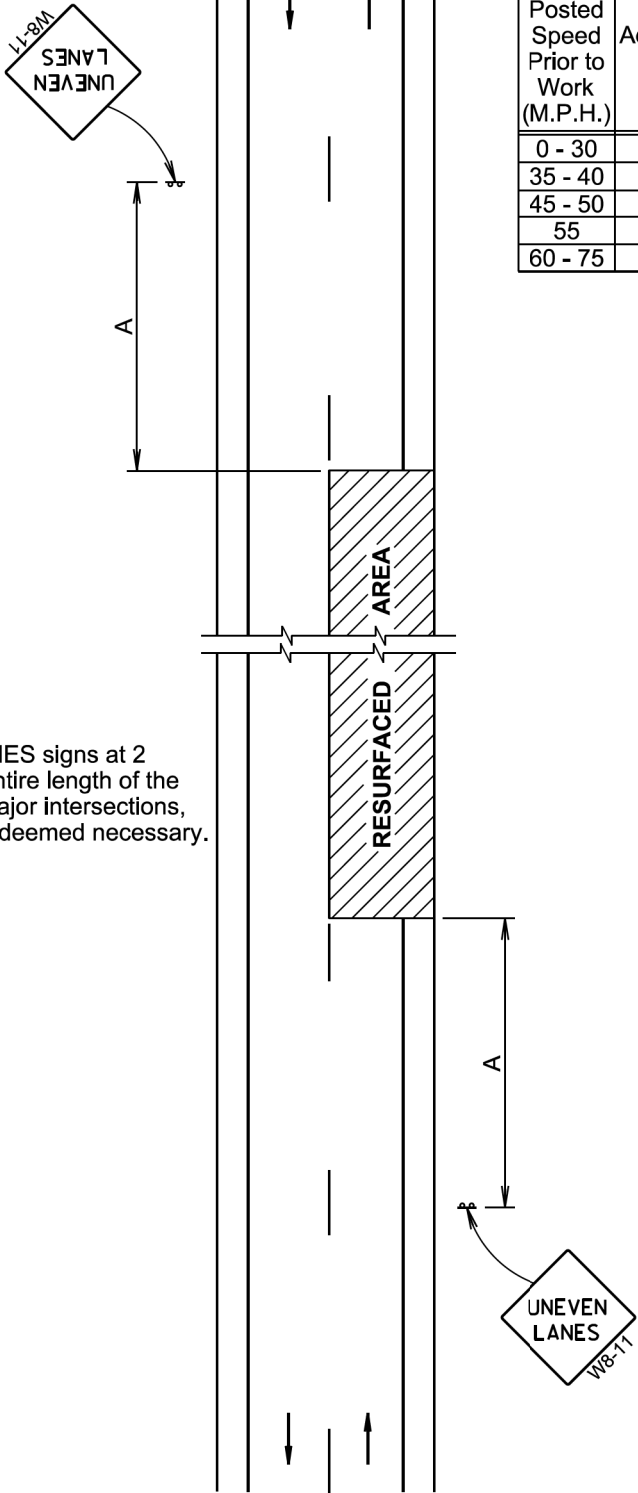


January 22, 2021

Published Date: 2024	S D D O T	UNEVEN ROAD SURFACE	PLATE NUMBER 634.22
			Sheet 1 of 1

STATE OF SOUTH DAKOTA	PROJECT	SHEET	TOTAL SHEETS
	EM 0073(73)62		

Plotting Date: 04/04/2024

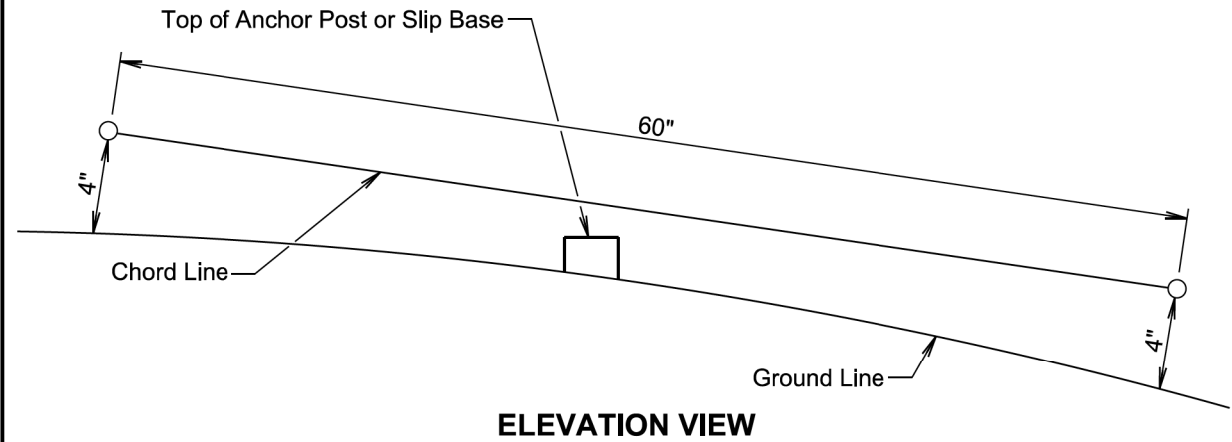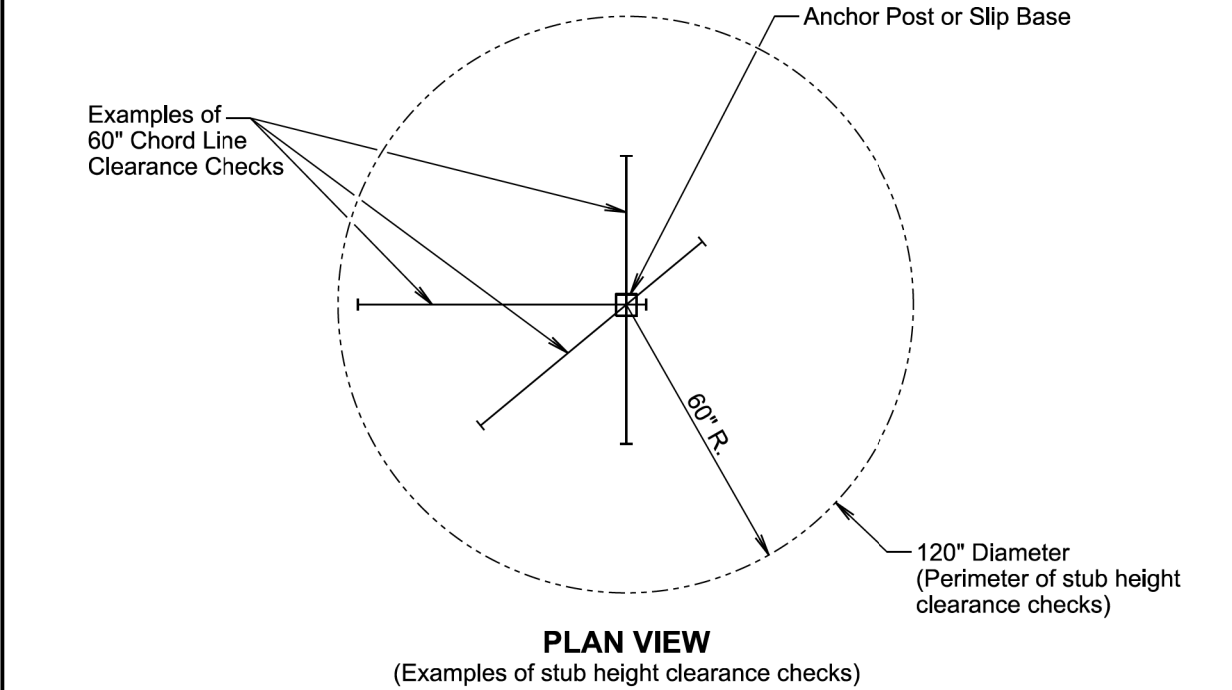

GENERAL NOTES:

The top of anchor posts and slip bases WILL NOT extend above a 60" chord line within a 120" diameter circle around the post with ends 4" above the ground.

At locations where there is curb and gutter adjacent to the breakaway sign support, the stub height will be a maximum of 4" above the ground line at the localized area adjacent to the breakaway support stub.

The 4" stub height clearance is not necessary for U-channel lap splices where the support is designed to yield (bend) at the base.

January 22, 2021

<i>Published Date: 2024</i>	S D D O T	BREAKAWAY SUPPORT STUB CLEARANCE	PLATE NUMBER 634.99
			Sheet 1 of 1
