

Department of Transportation

Office of Project Development

700 E Broadway Avenue

Pierre, South Dakota 57501-2586 605/773-3268

FAX: 605/773-2614

January 15, 2016

ADDENDUM NO. 1

RE: Item #6, January 20, 2016 Letting - P 0028(32)319, PCN 02QK, Clark, Hamlin County - Cold Milling Asphalt Concrete, Asphalt Concrete Resurfacing, ADA Upgrades, and Drainage Improvements

TO WHOM IT MAY CONCERN:

The following addenda to the plans shall be inserted and made a part of your proposal for the referenced project.

SPECIAL PROVISIONS: Please remove the Special Provisions checklist and replace with attached Special Provisions checklist revised 1/15/16.

Please remove the "Special Provision for Contract Time", dated 12/23/15 and replace with the "Special Provision for Contract Time", dated 1/14/16.

BID ITEM FILE: NO CHANGE

PLANS: NO CHANGE

Sincerely,

Sam Weisgram
Engineering Supervisor

SW/cj

CC: Jeff Senst, Aberdeen Region Engineer
Matt Brey, Watertown Area Engineer

REV. 1/15/16

SPECIAL PROVISIONS

PROJECT NUMBER(S): P 0028(32)319 PCN: 02QK

TYPE OF WORK: COLD MILLING ASPHALT CONCRETE, ASPHALT CONCRETE
RESURFACING, ADA UPGRADES, AND DRAINAGE IMPROVEMENTS

COUNTIES: CLARK, HAMLIN

The following clauses have been prepared subsequent to the Standard Specifications for Roads and Bridges and refer only to the above described improvement, for which the following Proposal is made.

The Contractor's attention is directed to the need for securing from the Department of Environment & Natural Resources, Foss Building, Pierre, South Dakota, permission to remove water from public sources (lakes, rivers, streams, etc.). The Contractor should make his request as early as possible after receiving his contract, and insofar as possible at least 30 days prior to the date that the water is to be used.

Sue Bogen is the official in charge of the Watertown Career Center for Clark, Hamlin Counties.

THE FOLLOWING ITEMS ARE INCLUDED IN THIS PROPOSAL FORM:

Special Provision for Contract Time, dated 1/14/16.

Special Provision for Subletting of Contract, dated 12/17/15.

Special Provision for Flexible Pavement Smoothness, dated 7/21/15.

Special Provision Regarding Section 404 of the Clean water Act, dated 12/17/15.

Fact Sheet #23.

List of Utilities.

Special Provision for Contractor Administered Preconstruction Meeting, dated 4/18/13.

Fuel Adjustment Affidavit, DOT form 208 dated 7/15.

Standard Title VI Assurance, dated 7/14/08.

Special Provision For Disadvantaged Business Enterprise, dated 5/20/15.

Special Provision For EEO Affirmative Action Requirements on Federal and Federal-aid Construction Contracts, dated 9/1/97.

Special Provision For Required Contract Provisions Federal-aid Construction Contracts, Form FHWA 1273 (Rev. May/1/12), dated 4/30/13.

Required Contract Provisions Federal-aid Construction Contracts, Form FHWA 1273 (Rev. 5/1/12).

Special Provision Regarding Minimum Wage on Federal-Aid Projects, dated 4/30/13.

Wage and Hour Division US Department of Labor Washington DC.

- US Dept. of Labor Decision Number SD150001, dated 10/9/15.

Special Provision for Price Schedule for Miscellaneous Items, dated 10/14/15.

Special Provision Regarding Storm Water Discharge, dated 5/3/13.

General Permit for Storm Water Discharges Associated with Construction

Activities, dated 2/1/10. <http://denr.sd.gov/des/sw/IPermits/ConstructionGeneralPermit2010.pdf>

* * * *

**STATE OF SOUTH DAKOTA
DEPARTMENT OF TRANSPORTATION**

**SPECIAL PROVISION
FOR
CONTRACT TIME**

**PROJECT P 0028(32)319; PCN 02QK
CLARK & HAMLIN COUNTIES**

JANUARY 14, 2016

Work in Bryant Calendar Day Count Requirement

The Contractor will complete the work specified in Bryant within 60 calendar days. The Department will begin to count calendar days when the Contractor begins work within the city limits of Bryant. The Department will continue to count calendar days until the Contractor completes the work required for and completes the first lift of asphalt concrete within the city limits of Bryant. The Department will count calendar days in accordance with Section 8.6 B.

If the Contractor does not complete the work required within the calendar day completion requirement, the Department will make a disincentive assessment in the amount of \$500 per calendar day.

Culvert Replacement Working Day Count Requirements

The Contractor will complete all work required for each culvert replacement within 2 working days per culvert replacement site. The Department will begin to count working days at each site when the Contractor begins the surface removal for the culvert removal/replacement work at each site. The Department will continue to count working days until the Contractor completes the work and normal traffic can move unimpeded at the culvert replacement site. The Contractor may use base course as a driving surface to restore normal traffic at the culvert replacement site. In addition, the Contractor will not perform the culvert removal or replacement work on a Saturday or holiday. The Department will count working days in accordance with Section 8.6 A.

If the Contractor does not complete the work within the 2 working day completion requirement, the Department will make a disincentive assessment in the amount of \$500 per working day.

In addition, the Contractor will complete all culvert replacements within 14 working days. The Department will begin to count working days when the Contractor begins the surface removal for the culvert removal or replacement work at the first culvert replacement site. The Department will continue to count working days until the

Contractor completes the work and completes the placement of 5 inches of asphalt concrete composite surfacing at all culvert replacement sites. The Department will count working days in accordance with Section 8.6 A.

If the Contractor does not complete the work within the 14 working day completion requirement, the Department will make a disincentive assessment in the amount of \$500 per working day.

Substantial Completion

The Contractor will substantially complete the project by the October 14, 2016 substantial completion date.

The Department will consider the work substantially complete in accordance with Section 8.6.

The Engineer, in his or her sole discretion will determine when the project is substantially complete.

Field Work Completion

The Contractor will complete the project by the October 21, 2016 field work completion date.

Time Extensions

In order to avoid or reduce liquidated damage and disincentive assessments, the Contractor may request a time extension for the calendar day count requirement, working day count requirement, substantial completion requirement, and field work completion requirement. The Department will consider these time extension requests using the same considerations that apply when granting an extension of contract time under Section 8.7, except extra work or an increase in quantities will not qualify for an automatic extension of time based on a proportional

Failure to Complete on Time

The Contractor will substantially complete the project prior to the substantial completion requirement or the substantial completion requirement as amended by formally approved time extensions. If the Contractor does not complete the work by the substantial completion requirement or the substantial completion requirement as amended by formally approved time extensions, the Department will assess liquidated damages in accordance with Section 8.8 Table A. The Department will assess liquidated damages for each working day the work (project) is late until the Contractor substantially completes the work.

In the event the Contractor does not substantially complete the work on time, the Department will count working days in accordance with Section 8.6 C.

The Contractor will complete all work on the project prior to the field work completion requirement or the field work completion requirement as amended by formally approved time extensions. If the Contractor does not complete all work by the field work completion requirement or the field work completion requirement as amended by formally approved time extensions, the Department will assess liquidated damages in accordance with Section 8.8. The Department will assess liquidated damages for each working day the work (project) is late until the Contractor completes all field work.

In the event the Contractor does not complete all field work on time, the Department will count working days in accordance with Section 8.6 C.

Expected Adverse Weather Days

The Department has provided Attachment 1 for information purposes only as a guide to bidders. This table depicts the typical number of adverse weather days expected for any given month, based on historical records. The Department will consider this project a surfacing project in Zone 6.

The Department will consider expected adverse weather days cumulative in nature over the time period when the Contractor is actively pursuing completion of the work. The Department will not consider adverse weather days during an extended period of time when the Contractor is not pursuing completion of the work. When considering a time extension for calendar day count completion, working day count completion, substantial completion or field work completion requirements of the project, the Engineer will compare the total number of expected adverse weather days against the total number of actual adverse weather days for the time period during which the work was being completed.

* * * * *

ATTACHMENT 1

Figure A - Expected Adverse Weather Days for South Dakota

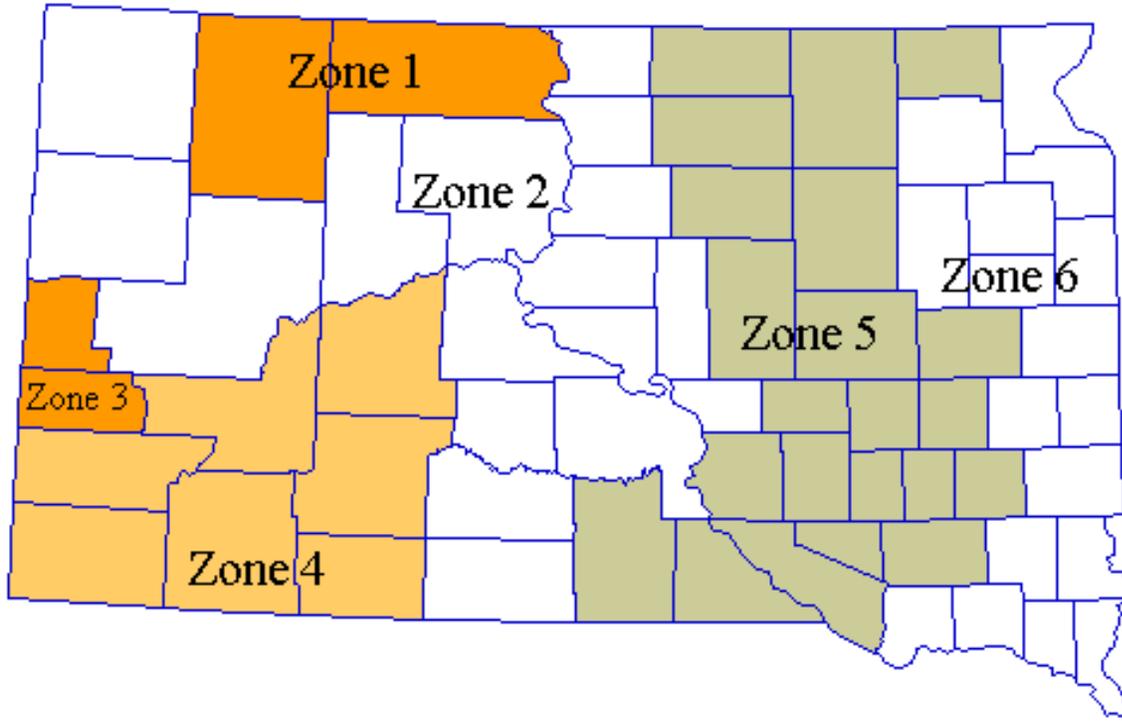


Table 1 - Expected Adverse Weather Days for South Dakota

	Grading Projects						Surfacing and Structural Projects					
	Zone 1	Zone 2	Zone 3	Zone 4	Zone 5	Zone 6	Zone 1	Zone 2	Zone 3	Zone 4	Zone 5	Zone 6
Jan	18	18	16	16	22	24	18	18	15	16	21	23
Feb	19	18	12	14	19	21	19	18	12	14	19	21
Mar	12	10	9	8	11	13	12	10	9	8	10	12
Apr	6	5	8	5	6	6	5	4	6	4	4	4
May	6	6	8	6	6	6	5	5	6	4	4	5
Jun	7	6	7	6	7	8	5	5	5	4	5	6
Jul	5	5	6	5	6	7	4	4	5	3	4	5
Aug	4	4	5	4	5	6	3	3	4	3	4	4
Sep	3	3	4	3	4	5	2	2	3	2	3	4
Oct	4	3	5	3	4	4	3	3	4	2	3	3
Nov	11	9	8	7	10	12	11	9	8	7	10	11
Dec	21	19	15	14	20	22	21	19	15	14	20	22

NOTE: Includes Holidays and Weekends.
