



Planning & Engineering
Office of Project Development
700 E Broadway Avenue
Pierre, South Dakota 57501-2586
O: 605.773.3275 | F: 605.773.2614
dot.sd.gov

November 25, 2024

ADDENDUM NO. 1

**RE: Item #3, December 4, 2024 Letting - NH-P-PH 0079(87)129, NH 0212(193)28, PCN 04L0,
06CP, Butte County - Grading, Asphalt Concrete Surfacing & Resurfacing**

TO WHOM IT MAY CONCERN:

The following addenda to the plans shall be inserted and made a part of your proposal for the referenced project.

SPECIAL PROVISIONS: Please remove the Index of Special Provisions and replace with attached Index of Special Provisions revised 11/15/24.

Please add the "Special Provision for Contract Time", dated 11/15/24 before the "Special Provision Regarding Combination Bids", dated 11/5/24.

SDEBS BID PROPOSAL: NONE

PLANS: NONE

Sincerely,

Sam Weisgram
Engineering Supervisor

SW/cj

CC: Todd Seaman, Rapid City Region Engineer
John Matthesen, Belle Fourche Area Engineer

REV 11/15/24

INDEX OF SPECIAL PROVISIONS

PROJECT NUMBER(S): NH-P-PH 0079(87)129, NH 0212(193)28 PCN: 04L0, 06CP

TYPE OF WORK: GRADING, ASPHALT CONCRETE SURFACING & RESURFACING

COUNTY: BUTTE

The following clauses have been prepared subsequent to the Standard Specifications for Roads and Bridges and refer only to the above described improvement, for which the following Proposal is made.

The Contractor's attention is directed to the need for securing from the Department of Environment & Natural Resources, Foss Building, Pierre, South Dakota, permission to remove water from public sources (lakes, rivers, streams, etc.). The Contractor should make his request as early as possible after receiving his contract, and insofar as possible at least 30 days prior to the date that the water is to be used.

Jonathan England is the official in charge of the Spearfish Career Center for Butte County.

THE FOLLOWING ITEMS ARE INCLUDED IN THIS PROPOSAL FORM:

Special Provision for Contract Time, dated 11/15/24.

Special Provision Regarding Combination Bids, dated 11/5/24.

Special Provision for Alternate Bidding, dated 11/7/24.

Special Provision Regarding Section 404 of the Clean Water Act, dated 10/31/24.

Fact Sheet #3.

Special Provision for On-The-Job Training Program, dated 3/10/16.

Special Provision for Flexible Pavement Smoothness, dated 5/20/21.

**Special Provision for Contractor Staking with Machine
Control Grading Option, dated 11/5/24.**

List of Utilities.

Special Provision for Steel Beam Guardrail AASHTO M 180 Designation, date 10/8/24.

Special Provision for Acknowledgment and Certification Regarding Article 3, Section 12 of the South Dakota Constitution, dated 8/24/23.

Special Provision for Buy America, dated 5/1/24.

Special Provision for Liability Insurance, dated 4/21/22.

Special Provision for Responsibility for Damage Claims, dated 4/21/22.

Special Provision for Restriction of Boycott of Israel, dated 1/31/20.

Special Provision for Contractor Administered Preconstruction Meeting, dated 12/18/19.
Fuel Adjustment Affidavit, DOT form 208 dated 7/15.
Standard Title VI Assurance, dated 3/1/16.
Special Provision For Disadvantaged Business Enterprise, dated 2/9/24.
Special Provision For EEO Affirmative Action Requirements on Federal and Federal-Aid Construction Contracts, dated 2/5/24.
Special Provision For Required Contract Provisions Federal-Aid Construction Contracts, Form FHWA 1273 (Rev. October 23, 2023), dated 10/18/23.
Required Contract Provisions Federal-Aid Construction Contracts, Form FHWA 1273 (Rev. 10/23/23).
Special Provision Regarding Minimum Wage on Federal-Aid Projects, dated 10/24/19.
Wage and Hour Division US Department of Labor Washington DC. - US Dept. of Labor Decision Number SD20230032, dated 3/10/23.
Special Provision for Supplemental Specifications to 2015 Standard Specifications for Roads and Bridges, dated 9/7/22.
Special Provision for Price Schedule for Miscellaneous Items, dated 12/6/23.

Special Provision Regarding Storm Water Discharge, dated 5/8/18.
General Permit for Storm Water Discharges Associated with Construction Activities, dated 4/1/18
<https://danr.sd.gov/OfficeOfWater/SurfaceWaterQuality/stormwater/StormWaterConstruction.aspx>

**STATE OF SOUTH DAKOTA
DEPARTMENT OF TRANSPORTATION**

**SPECIAL PROVISION
FOR
CONTRACT TIME**

**PROJECT NH-P-PH 0079(87)129 & NH 0212(193)28; PCN 04L0 & 06CP
BUTTE COUNTY**

NOVEMBER 15, 2024

Sturgis Motorcycle Rally Restrictions

The Contractor will open all lanes to through traffic on the project from July 26, 2025 to August 10, 2025 (inclusive) due to the Sturgis Motorcycle Rally.

The Contractor will not expose traffic to differential elevations in traveling lanes during this timeframe. The Contractor will place a minimum of 4 inches of granular material on all newly graded sections. The Department will not allow milled surfaces, grooved surfaces, uneven lanes, or shoulder drop offs during this timeframe.

The Department will make a disincentive assessment in the amount of \$1,000 per calendar day for the Contractor's failure to comply with the Sturgis Motorcycle Rally restrictions. A contract item for incentive/disincentive pay is included in the bid schedule for the Department's use in assessing disincentive. The Department will use a negative quantity of days for assessing disincentives. The Department will not grant time extensions for the Sturgis Motorcycle Rally restrictions for any reason.

Field Work Completion

The Contractor will complete the project by the November 14, 2025 field work completion date.

Failure to Complete on Time

The Contractor will complete all work on the project prior to the field work completion requirement or the field work completion requirement as amended by formally approved time extension. If the Contractor does not complete all work by the field work completion requirement or the field work completion requirement as amended by formally approved time extension, the Department will assess liquidated damages in accordance with Section 8.8. The Department will assess liquidated damages for each working day the work (project) is late until the Contractor completes all field work.

In the event the Contractor does not complete all field work on time, the Department will count working days in accordance with Section 8.6 C.

Expected Adverse Weather Days

The Department has provided Attachment 1 for information purposes only as a guide to bidders. This table depicts the typical number of adverse weather days expected for any given month, based on historical records. The Department will consider this project a grading project in Zone 2.

The Department will consider expected adverse weather days cumulative in nature over the time period when the Contractor is actively pursuing completion of the work. The Department will not consider adverse weather days during an extended period of time when the Contractor is not pursuing completion of the work. When considering a time extension for field work completion of the project, the Engineer will compare the total number of expected adverse weather days against the total number of actual adverse weather days for the time period during which the work was being completed.

* * * * *

ATTACHMENT 1

Figure A - Expected Adverse Weather Days for South Dakota

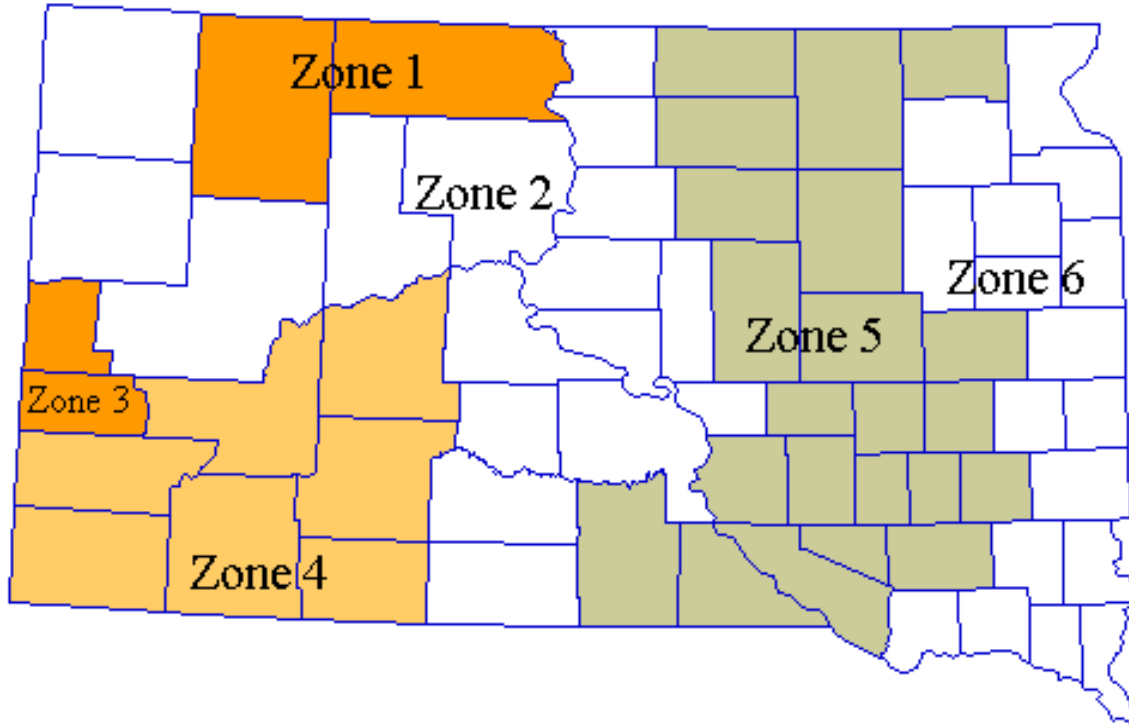


Table 1 - Expected Adverse Weather Days for South Dakota

	Grading Projects						Surfacing and Structural Projects					
	Zone 1	Zone 2	Zone 3	Zone 4	Zone 5	Zone 6	Zone 1	Zone 2	Zone 3	Zone 4	Zone 5	Zone 6
Jan	18	18	16	16	22	24	18	18	15	16	21	23
Feb	19	18	12	14	19	21	19	18	12	14	19	21
Mar	12	10	9	8	11	13	12	10	9	8	10	12
Apr	6	5	8	5	6	6	5	4	6	4	4	4
May	6	6	8	6	6	6	5	5	6	4	4	5
Jun	7	6	7	6	7	8	5	5	5	4	5	6
Jul	5	5	6	5	6	7	4	4	5	3	4	5
Aug	4	4	5	4	5	6	3	3	4	3	4	4
Sep	3	3	4	3	4	5	2	2	3	2	3	4
Oct	4	3	5	3	4	4	3	3	4	2	3	3
Nov	11	9	8	7	10	12	11	9	8	7	10	11
Dec	21	19	15	14	20	22	21	19	15	14	20	22

NOTE: Includes Holidays and Weekends.
