



Planning & Engineering
Office of Project Development
700 E Broadway Avenue
Pierre, South Dakota 57501-2586
O: 605.773.3275 | F: 605.773.2614
dot.sd.gov

April 2, 2025

ADDENDUM NO. 1

**RE: Item #2, April 16, 2025 Letting - NH 0018(239)244, P 0049(10)42, PCN 08H9, 08HC, Tripp
County - LSDC Overlay**

TO WHOM IT MAY CONCERN:

The following addenda to the plans shall be inserted and made a part of your proposal for the referenced project.

SPECIAL PROVISIONS: PEN AND INK change the FIELD WORK COMPLETION from NOVEMBER 7, 2025 to SEPTEMBER 4, 2026 on the NOTICE TO CONTRACTORS.

Please remove the Index of Special Provisions and replace with attached Index of Special Provisions revised 4/2/25. "Special Provision for Contract Time" dated 4/2/25 was added.

Please add the Special Provision for Contract Time" dated 4/2/25 before the "Special Provision for Prosecution and Progress", dated 1/21/21.

SDEBS BID PROPOSAL: *The electronic bid proposal for this contract has been revised to include the changes associated with this addendum. Bidders must log in to the SDEBS to retrieve and incorporate these changes into their bid.*

Bid Items were added:
Bid Item 009E1000 "Incentive/Disincentive Pay"

PLANS: NO CHANGE

Sincerely,

Sam Weisgram
Engineering Supervisor

SW/cj

CC: Jason Humphrey, Pierre Region Engineer
Doug Sherman, Winner Area Engineer

REV 4/2/25

INDEX OF SPECIAL PROVISIONS

PROJECT NUMBER(S): NH 0018(239)244, P 0049(10)42 PCN: 08H9, 08HC

TYPE OF WORK: LSDC OVERLAY

COUNTY: TRIPP

The following clauses have been prepared subsequent to the Standard Specifications for Roads and Bridges and refer only to the above described improvement, for which the following Proposal is made.

The Contractor's attention is directed to the need for securing from the Department of Environment & Natural Resources, Foss Building, Pierre, South Dakota, permission to remove water from public sources (lakes, rivers, streams, etc.). The Contractor should make his request as early as possible after receiving his contract, and insofar as possible at least 30 days prior to the date that the water is to be used.

Bobbie Country is the official in charge of the Winner Career Center for Tripp County.

THE FOLLOWING ITEMS ARE INCLUDED IN THIS PROPOSAL FORM:

Special Provision for Contract Time, dated 4/2/25.

Special Provision for Prosecution and Progress, dated 1/21/21.

Special Provision for Traffic Control Supervisor, dated 3/13/25.

Special Provision for Steel Beam Guardrail AASHTO M 180 Designation, date 10/8/24.

Special Provision for Acknowledgment and Certification Regarding Article 3, Section 12 of the South Dakota Constitution, dated 8/24/23.

Special Provision for Buy America, dated 5/1/24.

Special Provision for Liability Insurance, dated 4/21/22.

Special Provision for Responsibility for Damage Claims, dated 4/21/22.

Special Provision for Restriction of Boycott of Israel, dated 1/31/20.

Special Provision for Contractor Administered Preconstruction Meeting, dated 12/18/19.

Fuel Adjustment Affidavit, DOT form 208 dated 7/15.

Standard Title VI Assurance, dated 3/1/16.

Special Provision For Disadvantaged Business Enterprise, dated 2/9/24.

Special Provision For EEO Affirmative Action Requirements on Federal and Federal-Aid Construction Contracts, dated 2/5/24.

Special Provision For Required Contract Provisions Federal-Aid Construction Contracts, Form FHWA 1273 (Rev. October 23, 2023), dated 10/18/23.

Required Contract Provisions Federal-Aid Construction Contracts, Form FHWA 1273 (Rev. 10/23/23).

Special Provision Regarding Minimum Wage on Federal-Aid Projects, dated 10/24/19.

Wage and Hour Division US Department of Labor Washington DC. - US Dept. of Labor Decision
Number SD20230032, dated 3/10/23.

Special Provision for Supplemental Specifications to 2015 Standard Specifications for
Roads and Bridges, dated 9/7/22.

Special Provision for Price Schedule for Miscellaneous Items, dated 12/6/23.

**STATE OF SOUTH DAKOTA
DEPARTMENT OF TRANSPORTATION**

**SPECIAL PROVISION
FOR
CONTRACT TIME**

**PROJECT NH 0018(239)244 & P 0049(10)42; PCN 08H9 & 08HC
TRIPP COUNTY**

APRIL 2, 2025

Field Work Completion

The Contractor will complete the project by the September 4, 2026 field work completion date.

October 31, 2025 Interim Completion Requirement

The Contractor will complete all the work and have traffic fully restored to the roadway on Str. No. 62-115-270, Str. No. 62-149-270, & Str. No. 62-183-274 on the project by the October 31, 2025 interim completion date.

If the Contractor elects to begin work at any other site in 2025, the Contractor will complete all work at that site and have traffic fully restored to the roadway by the October 31, 2025 interim completion date.

If the Contractor does not complete the work by the interim completion requirement, the Department will make a disincentive assessment in the amount of \$500 per working day. A contract item for incentive/disincentive pay is included in the bid schedule for the Department's use in assessing disincentive. The Department will use a negative quantity of days for assessing disincentives. The Department will count working days in accordance with Section 8.6 C.

Failure to Complete on Time

The Contractor will complete all work on the project prior to the field work completion requirement. If the Contractor does not complete all work by the field work completion requirement, the Department will assess liquidated damages in accordance with Section 8.8. The Department will assess liquidated damages for each working day the work (project) is late until the Contractor completes all field work.

In the event the Contractor does not complete all field work on time, the Department will count working days in accordance with Section 8.6 C.

Expected Adverse Weather Days

The Department has provided Attachment 1 for information purposes only as a guide to bidders. Table 1 depicts the typical number of adverse weather days expected for any given month, based on historical records. The Department will consider this project a surfacing project in Zone 5.

The Department will consider expected adverse weather days cumulative in nature over the time period when the Contractor is actively pursuing completion of the work. The Department will not consider adverse weather days during an extended period of time when the Contractor is not pursuing completion of the work. When considering a time extension for interim completion or field work completion of the project, the Engineer will compare the total number of expected adverse weather days against the total number of actual adverse weather days for the time period during which the work was being completed.

* * * * *

ATTACHMENT 1

Figure A - Expected Adverse Weather Days for South Dakota

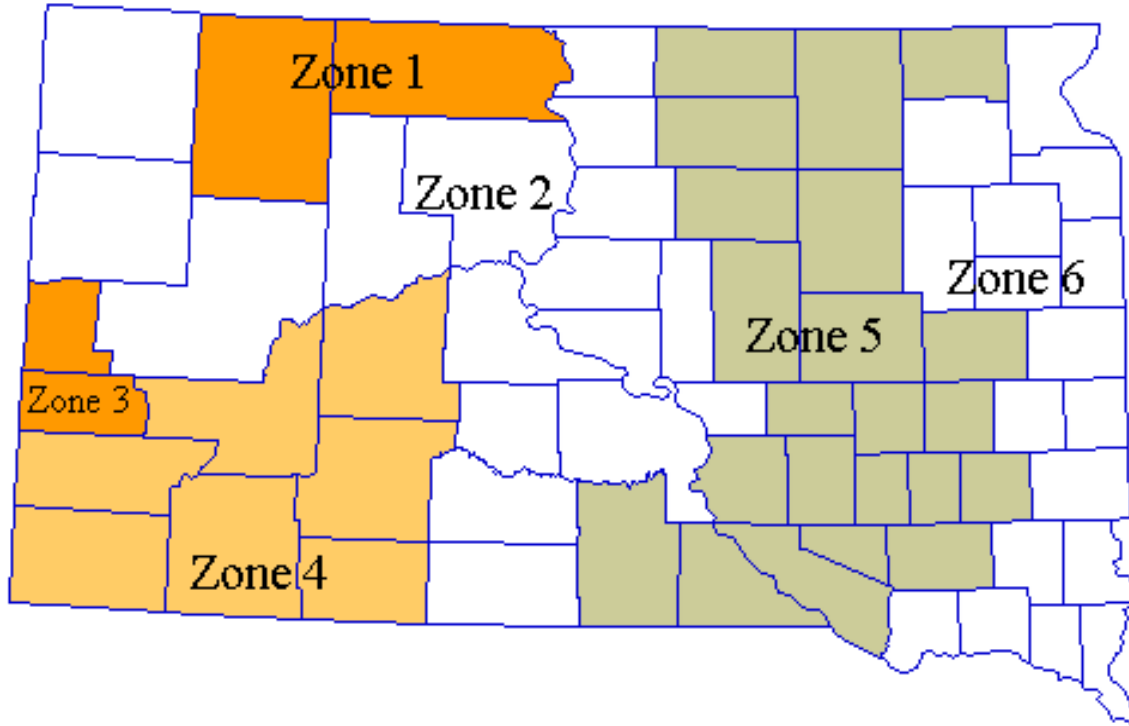


Table 1 - Expected Adverse Weather Days for South Dakota

	Grading Projects						Surfacing and Structural Projects					
	Zone 1	Zone 2	Zone 3	Zone 4	Zone 5	Zone 6	Zone 1	Zone 2	Zone 3	Zone 4	Zone 5	Zone 6
Jan	18	18	16	16	22	24	18	18	15	16	21	23
Feb	19	18	12	14	19	21	19	18	12	14	19	21
Mar	12	10	9	8	11	13	12	10	9	8	10	12
Apr	6	5	8	5	6	6	5	4	6	4	4	4
May	6	6	8	6	6	6	5	5	6	4	4	5
Jun	7	6	7	6	7	8	5	5	5	4	5	6
Jul	5	5	6	5	6	7	4	4	5	3	4	5
Aug	4	4	5	4	5	6	3	3	4	3	4	4
Sep	3	3	4	3	4	5	2	2	3	2	3	4
Oct	4	3	5	3	4	4	3	3	4	2	3	3
Nov	11	9	8	7	10	12	11	9	8	7	10	11
Dec	21	19	15	14	20	22	21	19	15	14	20	22

NOTE: Includes Holidays and Weekends.
