



# Department of Transportation

**Rapid City Region Office**

**2300 Eglin Street**

**P.O. Box 1970**

**Rapid City, SD 57709-1970**

**Phone: 605/394-2244**

**FAX: 605/394-1904**

September 29, 2015

## **ADDENDUM NO. 2**

RE: October 1, 2015 Rapid City Region Office Informal Letting  
P 0231(00)79, Pennington County, PCN 05a5  
Concrete Pavement Repair

### **TO WHOM IT MAY CONCERN:**

The following addenda to the plans shall be inserted and made part of your proposal for the referenced project.

### **PROPOSAL:**

- The completion date on the DOT-123 is July 15, 2016. The attached contract time special provision was changed to match the DOT-123..

Sincerely,

---

John Rehorst  
Region Design Engineer

**STATE OF SOUTH DAKOTA  
DEPARTMENT OF TRANSPORTATION**

**SPECIAL PROVISION  
FOR  
CONTRACT TIME**

**PROJECT P 0231(00)79; PCN 05A5  
PENNINGTON COUNTY**

**September 11, 2015**

---

The Contractor will complete all work on the project by the July 15, 2016 field work completion date.

**No Working Day Count Prior to December 1, 2015**

If the Contractor elects to start work prior to December 1, 2015, working days will not be charged. The Department would like to have some or all the work complete prior to this date. If there is no work, then the lanes shall be opened to unimpeded traffic.

**Working Day Count Completion Requirement after March 31, 2016**

If the Contractor elects to start work after March 31, 2016, the Contractor will have 30 working days for the construction of the project. The Department will begin to charge working days when the Contractor begins work. The Department will continue to charge working days until the Contractor completes the project. The Department will charge working days in accordance with Section 8.6 A.

If the Contractor does not complete the work within the working day completion requirement, the Department will assess liquidated damages in the amount of \$1500 per working day.

**Time Extensions**

In order to avoid or reduce liquidated damage assessments, the Contractor may request a time extension for the overall completion date (excluding the Sturgis Motorcycle Rally restriction). The Department will consider these time extension requests using the same considerations that apply when granting an extension of Contract Time under Section 8.6, except extra work or an increase in quantities will not qualify for an automatic extension of time based on a proportional increase in the contract amount.

### **Failure to Complete on Time**

The Contractor will complete all work on the project, including final cleaning up, prior to the overall completion date or the overall completion date as amended by formally approved time extensions. If the Contractor does not complete all work, including final cleaning up, by the overall completion date or the overall completion date as amended by formally approved time extensions, the Department will assess liquidated damages in accordance with Section 8.7. The Department will assess liquidated damages for each working day the work (project) is late until the Contractor completes all contract work, including final cleaning up.

In the event the Contractor does not complete the work (project) on time, the Department will charge working days in accordance with Section 8.6 B except that 8.6 B.7 will not apply.

### **Expected Adverse Weather Days**

The Department has provided Attachment 1 for information purposes only as a guide to bidders. This table depicts the typical number of adverse weather days expected for any given month, based on historical records. The Department will consider this project a surfacing project in Zone 3.

The Department will consider expected adverse weather days cumulative in nature over the total time available for contract completion. When considering a time extension for the overall completion date, the Engineer will compare the total number of expected adverse weather days against the total number of actual adverse weather days for the entire period during which the work was to be completed.

\* \* \* \* \*

# ATTACHMENT 1

Figure A - Expected Adverse Weather Days for South Dakota

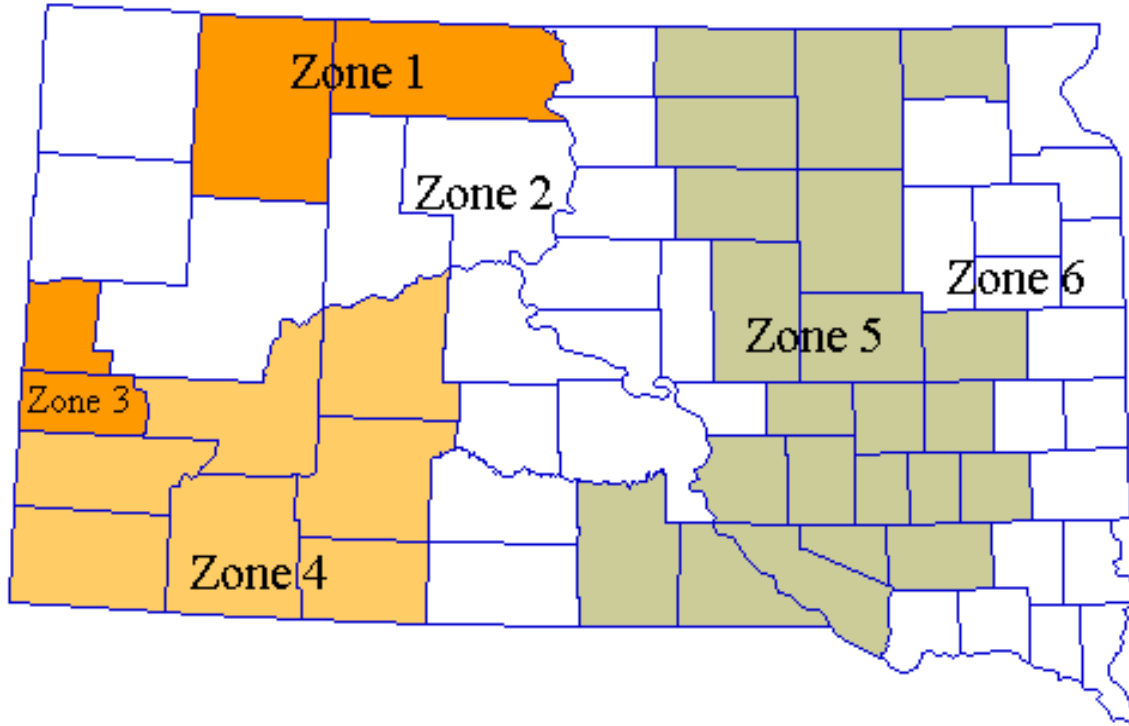


Table 1 - Expected Adverse Weather Days for South Dakota

	Grading Projects						Surfacing and Structural Projects					
	Zone 1	Zone 2	Zone 3	Zone 4	Zone 5	Zone 6	Zone 1	Zone 2	Zone 3	Zone 4	Zone 5	Zone 6
Jan	18	18	16	16	22	24	18	18	15	16	21	23
Feb	19	18	12	14	19	21	19	18	12	14	19	21
Mar	12	10	9	8	11	13	12	10	9	8	10	12
Apr	6	5	8	5	6	6	5	4	6	4	4	4
May	6	6	8	6	6	6	5	5	6	4	4	5
Jun	7	6	7	6	7	8	5	5	5	4	5	6
Jul	5	5	6	5	6	7	4	4	5	3	4	5
Aug	4	4	5	4	5	6	3	3	4	3	4	4
Sep	3	3	4	3	4	5	2	2	3	2	3	4
Oct	4	3	5	3	4	4	3	3	4	2	3	3
Nov	11	9	8	7	10	12	11	9	8	7	10	11
Dec	21	19	15	14	20	22	21	19	15	14	20	22

NOTE: Includes Holidays and Weekends.
