

Department of Transportation

Rapid City Region Office

2300 Eglin Street

P.O. Box 1970

Rapid City, SD 57709-1970

Phone: 605/394-2244

FAX: 605/394-1904

May 24, 2016

ADDENDUM NO. 1

RE: May 26, 2016 Rapid City Region Office Informal Letting
090W-451, 090E-451, 090E-452 & 090W-452,
Meade, Pennington & Jackson Counties
PCN i4cm, i4cn, i4dj & i4cp

TO WHOM IT MAY CONCERN:

The following addenda to the plans shall be inserted and made part of your proposal for the referenced project.

PROPOSAL:

- Please replace the Special Provision for Contract Time with the attached revised Special Provision for Contract Time.

PLANS:

- No change.

Sincerely,

John Rehorst
Region Design Engineer

**STATE OF SOUTH DAKOTA
DEPARTMENT OF TRANSPORTATION**

**SPECIAL PROVISION
FOR
CONTRACT TIME**

**PROJECT 090 W-451, 090 E-451, 090E-452, & 090W-452
PCNs i4cm, i4cn, i4dj, & i4cp
MEADE, PENNINGTON, and JACKSON COUNTIES**

May 24, 2016

The Contractor will complete all work on the project by the October 28, 2016 overall completion date.

Working Day Count Completion Requirement

In addition, the Contractor will have 30 working days for the construction of the project. The Department will begin to charge working days when the Contractor begins work. The Department will continue to charge working days until the Contractor completes the project. The Department will charge working days in accordance with Section 8.6 A.

If the Contractor does not complete the work within the working day completion requirement, the Department will assess liquidated damages in the amount of \$500 per working day.

Sturgis Motorcycle Rally Restrictions

In addition, the Contractor will open all lanes to unimpeded traffic and the Department will not allow work on the project from July 30, 2016 to August 15, 2016 (inclusive) due to the Sturgis Motorcycle Rally.

The Department will assess liquidated damages in the amount of \$1000 per calendar day for the Contractor's failure to comply with the Sturgis Motorcycle Rally restrictions. The Department will not grant time extensions for the Sturgis Motorcycle Rally restrictions for any reason.

Time Extensions

In order to avoid or reduce liquidated damage assessments, the Contractor may request a time extension for the working day completion requirement and overall completion date (excluding the Sturgis Motorcycle Rally restriction). The Department will consider these time extension requests using the same considerations that apply when granting an extension of Contract Time under Section 8.6, except extra work or an increase in

quantities will not qualify for an automatic extension of time based on a proportional increase in the contract amount.

Failure to Complete on Time

The Contractor will complete all work on the project prior to the working day completion requirement and overall completion date or the overall completion date as amended by formally approved time extensions. If the Contractor does not complete all work by the working day completion requirement and overall completion date or the overall completion date as amended by formally approved time extensions, the Department will assess liquidated damages in accordance with Section 8.7. The Department will assess liquidated damages for each working day the work (project) is late until the Contractor completes all contract work.

In the event the Contractor does not complete the work (project) on time, the Department will charge working days in accordance with Section 8.6 B.

Expected Adverse Weather Days

The Department has provided Attachment 1 for information purposes only as a guide to bidders. This table depicts the typical number of adverse weather days expected for any given month, based on historical records. The Department will consider this project a Sufacing project in Zone 4.

The Department will consider expected adverse weather days cumulative in nature over the time period when the Contractor is actively pursuing completion of the work. The Department will not consider adverse weather days during an extended period of time when the Contractor is not pursuing completion of the work. When considering a time extension for overall completion of the project, the Engineer will compare the total number of expected adverse weather days against the total number of actual adverse weather days for the time period during which the work was being completed.

* * * * *

ATTACHMENT 1

Figure A - Expected Adverse Weather Days for South Dakota

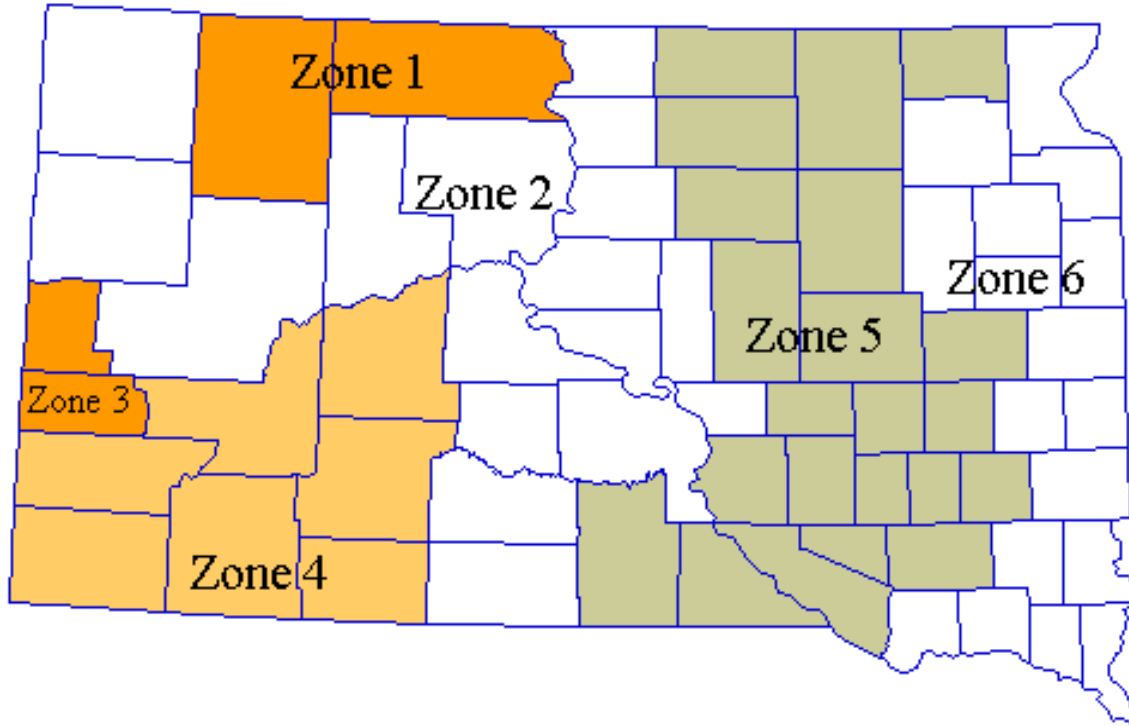


Table 1 - Expected Adverse Weather Days for South Dakota

	Grading Projects						Surfacing and Structural Projects					
	Zone 1	Zone 2	Zone 3	Zone 4	Zone 5	Zone 6	Zone 1	Zone 2	Zone 3	Zone 4	Zone 5	Zone 6
Jan	18	18	16	16	22	24	18	18	15	16	21	23
Feb	19	18	12	14	19	21	19	18	12	14	19	21
Mar	12	10	9	8	11	13	12	10	9	8	10	12
Apr	6	5	8	5	6	6	5	4	6	4	4	4
May	6	6	8	6	6	6	5	5	6	4	4	5
Jun	7	6	7	6	7	8	5	5	5	4	5	6
Jul	5	5	6	5	6	7	4	4	5	3	4	5
Aug	4	4	5	4	5	6	3	3	4	3	4	4
Sep	3	3	4	3	4	5	2	2	3	2	3	4
Oct	4	3	5	3	4	4	3	3	4	2	3	3
Nov	11	9	8	7	10	12	11	9	8	7	10	11
Dec	21	19	15	14	20	22	21	19	15	14	20	22

NOTE: Includes Holidays and Weekends.
